


Improvements On W Jackson Avenue And On Henley Street Project

Project Description: This project will consist of replacing approximately 5,500 square feet of concrete sidewalk on W Jackson Avenue and reconfiguring the median at Henley Street and W Church Avenue.



W Jackson Avenue - June 2016

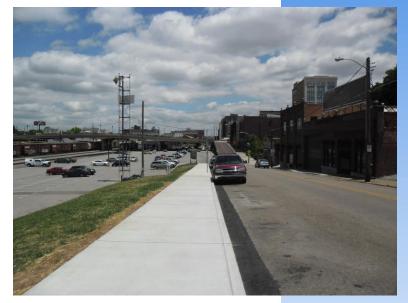

Henley Street - June 2016

Schedule:

Bid Opening: January 20, 2016 Notice to Proceed: April 11, 2016

Contract Completion Date: September 30, 2016

Current Contract Price: \$ 154,123

Engineering Department October 2016 Status: The project is complete. A change order to amend the contract is on the September 13, 2016 City Council agenda.

Project Designer: Cannon & Cannon, Inc.

Construction Contractor: McKinnon Construction Company, LLC

City of Knoxville Contact

Construction Engineer: Robin Tipton, PE (865) 215-6100



James R. Hagerman, PE Director of Engineering
