





2023 Pedestrian and Bicycle Pavement Marking Project

Project Description: This project will install 9,040 total feet of crosswalks, 4,350 feet of stop line markings, and 28 shared lane markings.

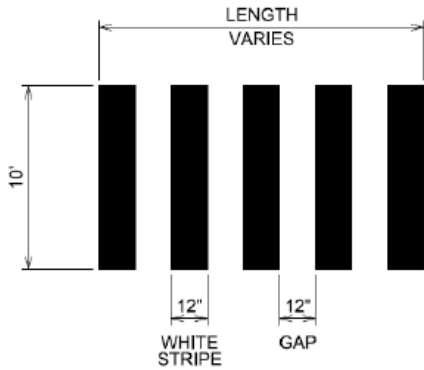


Note: Lines shall be parallel to direction of traffic

"CONTINENTAL STYLE" CROSSWALK
N.T.S.

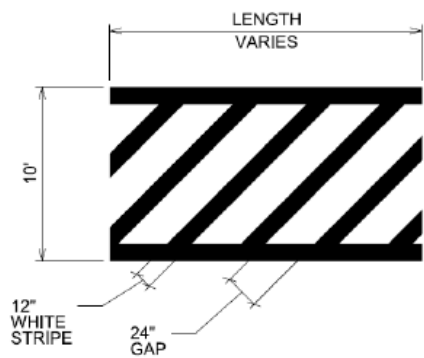

"DIAGONAL STYLE" CROSSWALK
N.T.S.

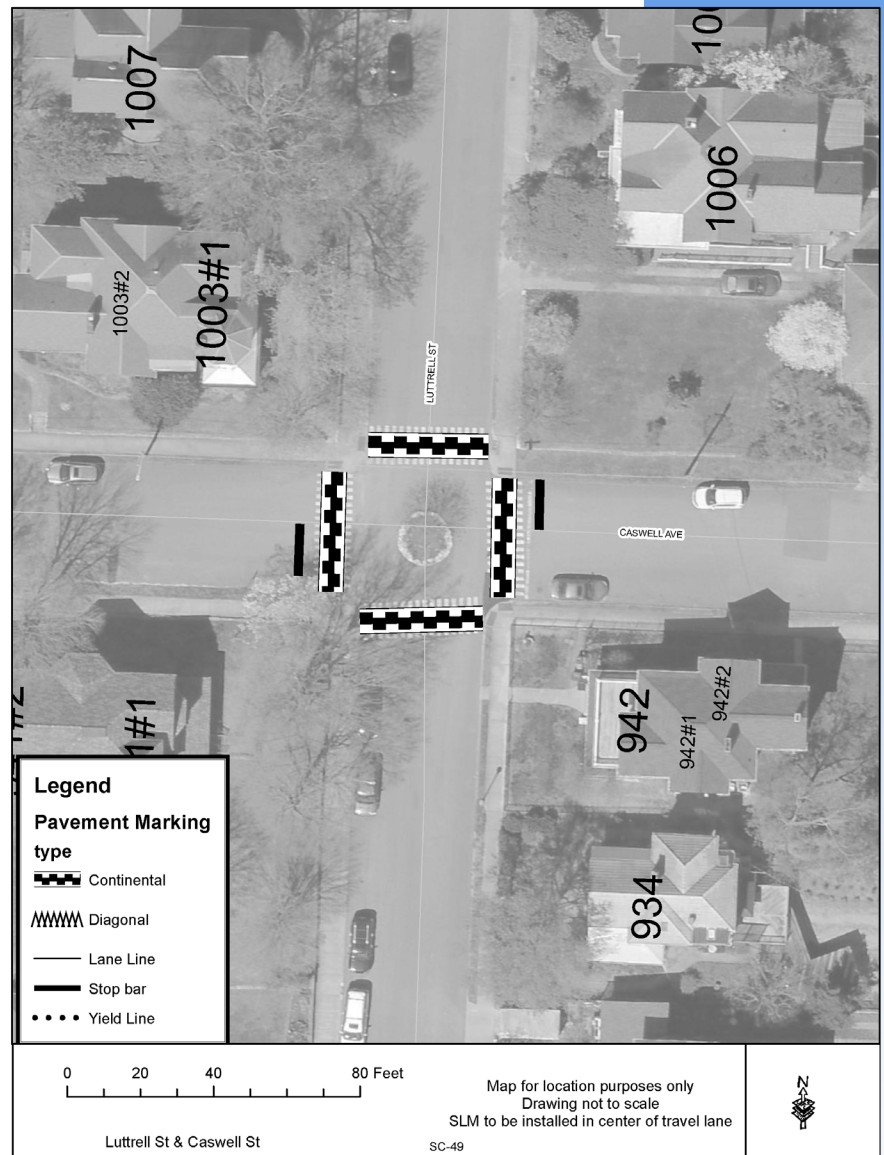

One of the 87 sites throughout the City

Schedule:

Bid Opening: May 24, 2023

Notice to Proceed: September 11, 2023

Contract Completion Date: November 10, 2023

Current Construction Contract Price: \$206,621

Engineering Department November 2023 Status: This construction contract was approved at the June 27, 2023 City Council Meeting. This project is 95% complete.

Project Designer: City of Knoxville

Construction Contractor: Superior Pavement Marking, Inc.

City of Knoxville Contact: Jon Livengood (865) 215-6100



CITY OF KNOXVILLE

Indya Kincannon, Mayor

W. Harold Cannon, Jr., P.E.
Engineering Director
