streetscapes construction progress TWO-WEEK LOOK AHEAD

Two Week Look Ahead

Updated July 27, 2017

THE FINAL COUNTDOWN - RIBBON CUTTING AUGUST 17, 2017!

During the past week

- Eastbound, westbound, and turn lanes of Cumberland Avenue through the Streetscapes project are paved
- South 22nd, South 21t, Mountcastle, South 19th, and South 18th are paved
- Thermoplastic striping of Cumberland turn lanes nearly complete
- Stamped crosswalk at University Commons is complete
- Median plantings have begun and will continue as plants arrive (irrigation is in place to water plants)
- Fiber optic interconnect splices are complete

Over the next two weeks expect to see:

- Complete paving and final striping
- Complete median plantings (except for trees, which will be installed late October)
- Install gateway monument signs
- Complete punch list items
- Install stamped crosswalks, starting at 17th Street intersection and working west (nights)
- Stamped crosswalks starting at University Commons begin on 8/1/2017

Two Week Look Ahead

Updated July 27, 2017

THE FINAL COUNTDOWN BEGINS!

During the past week

- Milling on Cumberland Streetscapes project is complete as well as milling of Cumberland from 16th Street to Henley Street
- KUB sewer work in East Volunteer is complete
- Curbs and sidewalks at UT Student Center have been poured
- Stamped crosswalks at Volunteer (west) are complete
- Additional bollards are installed at Insomnia Cookies, Mellow Mushroom, and traffic cabinet at Melrose
- Sewer manhole in N19th and electrical manhole in N18th have been lowered
- All concrete punch list items have been resolved
- Bus shelter lighting areas with tactile warnings are complete

Fiber optic interconnect cable for traffic signals has been pulled from 17th to Metron Center Way

Over the next two weeks expect to see:

- Complete irrigation and begin planting medians
- Subcontractors will work on punch list items
- Final paving and striping of project
- Stamped crosswalks starting at University Commons begin on 8/1/2017

Two Week Look Ahead

Updated June 22, 2017

THE PROJECT IS NEARING COMPLETION!

During the past week

- All turn lanes are temporarily striped and open to traffic
- Asphalt patching against the new medians is complete
- All concrete in the medians has been poured to the end of the project
- Bench installation complete on the north side of Cumberland

Over the next two weeks expect to see:

- Rework curb line at the southeast corner of Cumberland at 17th
- Curbing at University Liquors
- Continue site furnishing installation

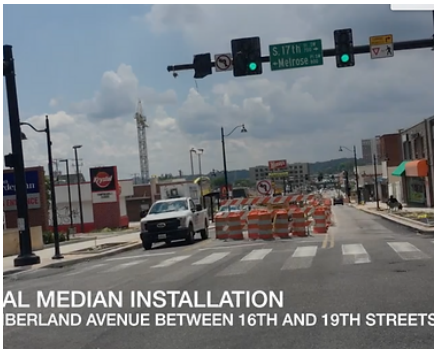

Two Week Look Ahead

Updated June 15, 2017

THE LAST SECTION NEARS COMPLETION!

During the past week

- Median curbs are complete from North 19th to the end of project
- Color median concrete poured from end of project to 25' west of 17th Street
- Bench installation has begun
- Paver installation is complete

Over the next two weeks expect to see:

- Complete median construction from North 19th to the end of project.
- Temporary striping to open turn lanes at 18th and 17th/Melrose before cycling event
- Continue site furnishing installation

Two Week Look Ahead

Updated June 8, 2017

THE LAST SECTION NEARS COMPLETION!

During the past week

- Repair work at the corner of Cumberland and 17th is complete
- Curb at Fedes/Kinkos has been re-poured to correct cross slope for bus shelter pad
- All five bus shelter frats have been installed

Over the next two weeks expect to see:

-

- Construct center medians from North 19th to the end of project
- Pave against center medians and open turn lanes at 18th and 17th/Melrose

Two Week Look Ahead

Updated June 1, 2017

THE LAST SECTION NEARS COMPLETION!

During the past week

- West alley entrance off South 21st has been re-poured
- Sidewalks on the west side of Melrose are complete
- Eastbound traffic is now permanently traveling along the south curb line
- Repair work at the corner of Cumberland and 17th is underway
- Service One has begun work for the additional north side street lighting (KUB)

Over the next two weeks expect to see:

- Split traffic from North 19th to the end of project to begin building the remaining center medians
- Begin center median construction from North 19th to the end of project
- Begin site furnishing installation

Two Week Look Ahead

Updated May 25, 2017

THE LAST SECTION NEARS COMPLETION!

During the past week

- Binder placement and driveway patching on Cumberland is complete
- Binder placement and driveway patching on side streets is complete except for the west side of Melrose and the west alley entrance off South 21st
- Sidewalks and handicap ramps at the SW corner of Melrose have been poured
- Sidewalks on the west side of Melrose will be poured today and tomorrow
- Fiber reinforced soil installed in the medians between North 21st and South 19th
- Pavers installed to last planter well on Cumberland

Over the next two weeks expect to see:

- Complete furnishing zone construction east of Melrose to end of project
- Complete sidewalks on west side of Melrose
- Shift traffic for repair work at the corner of 17th and Cumberland, 5/30/17, after the Destination Imagination event is over

Two Week Look Ahead

Updated May 18, 2017

THE LAST SECTION NEARS COMPLETION!

During the past week

- All curbs and sidewalks on South 18th have been poured
- Radius curb at Melrose has been poured
- First layer of median soil installed in the median between Mountcastle and South 19th

Gateway monuments on the west end of the project are complete
- Pavers installed to 1700 Melrose
- Paving of Cumberland from 1830 to end of project beginning Thursday, May 18, also paving along curbs and at utility cuts on south side streets

Over the next two weeks expect to see:

- Complete furnishing zone construction east of Melrose to end of project
- Install fiber reinforced median soil from 22nd to North 19th
- Complete sidewalks on Melrose
- Shift traffic at 17th to allow for repair work at the corner of 17th and Cumberland after Destination Imagination

Two Week Look Ahead

Updated May 11, 2017

THE LAST SECTION NEARS COMPLETION!

During the past week

- Entrance to Moe's off South 18th has been poured
- South alley entrance off the west side of South 18th is being poured
- Sidewalks at the Baker Center have been replaced
- First layer of median soil installed in the median between 21st and Mountcastle
- Gateway monuments on the east end of the project are nearly complete

Over the next two weeks expect to see:

- Complete furnishing zone construction east of Melrose to end of project
- Complete sidewalk construction along the west side of South 18th
- Continue to install median soil from 22nd to North 19th
- Pave binder in the south land of Cumberland to the end of project
- Begin sidewalks on Melrose

Two Week Look Ahead

UPDATED MAY 4, 2017

THE LAST SECTION NEARS COMPLETION!

During the past week

- Planter curbs are poured to the end of the project
- Pervious concrete is poured to the end of the project
- New signal system at 17th is active
- Pavers are installed to Krystal
- All utility pole removals and new street lighting on Cumberland is complete

Over the next two weeks expect to see:

- Complete furnishing zone construction east of Melrose to the end of project
- Sidewalk construction along the west side of South 18th
- Medial soil installation from 22nd to North 19th

Two Week Look Ahead

UPDATED APRIL 27, 2017

WE ARE GETTING CLOSER TO COMPLETION!

During the past week

- Roadway curbs along Cumberland poured to the end
- Sidewalks on Cumberland poured to the end
- Pervious concrete poured to Melrose
- Silva cell installation completed
- New signal system at 17th completed
- West end gateway monuments completed

Over the next two weeks expect to see:

- Continue furnishing zone construction east of Melrose to the end
- Sidewalk construction along the west side of South 18th
- Medial soil installation from 22nd to North 19th

Two Week Look Ahead

UPDATED APRIL 20, 2017

WE ARE GETTING CLOSER TO COMPLETION!

During the past week

- West entrance to Krystal is complete
- Sidewalks are poured to the radius at Melrose
- Planter curbs are poured to Krystal
- Silva cell installation is nearly complete - one planter at 17th remains
- Pavers are installed to McDonalds
- New street lighting and wiring installed to McDonalds
- East end gateway monuments stacked out to cap stones, tuck pointing ongoing

Over the next two weeks expect to see:

- Continue sidewalk construction east of Melrose to end of project
- Change over traffic signals at 17th to new system on Thursday April 27, 2017
- Median soil installation from 22nd to North 19th

Two Week Look Ahead

UPDATED APRIL 13, 2017

WE ARE GETTING CLOSER TO COMPLETION!

During the past week

- Westbound turn lane at 22nd striped and open to traffic
- East entrance to Krystal and the entrance to Hilton Garden Inn are complete
- Roadway curbs are poured from catch basin 35 to the radius at Melrose
- Pervious concrete is poured to Krystal
-

Silva sell excavation is complete

Pavers are installed to South 18th

New street lighting and wiring installed to South 18th

Both west end gateway monuments have stone stacked out to just below masonry cap

Over the next two weeks expect to see:

Continue sidewalk construction to Melrose then across Melrose to end of project

Complete silva cell installations east of Melrose

Change over traffic signals at 17th to new system, tentatively scheduled for Friday, April 21

Median soil installation from 22nd to North 19th

Two Week Look Ahead

UPDATED APRIL 6, 2017

PLEASE BE AWARE AND SHARE...

During the past week

FULL DEPTH EXCAVATION AND REBUILD OF SOUTH 18TH IS COMPLETE

Colored concrete is poured in all medians from 22nd to North 19th

Roadway curbs, sidewalks, and all colored concrete is poured through the west entrance of McDonalds

Electrical vault at the alley on South 19th has been lowered

Electrical service conversions in South 19th are complete

Silva cells at Firehouse is complete

Pavers are installed to Wendy's

All four gateway monument structural solumns are complete, masons are working on stone mock-up at the Metron Center Way monument

Over the next two weeks expect to see:

Continue sidewalk construction to Melrose

Irrigation and fiber reinforced planting soils in medians between 21st and South 19th

Complete sidewalks on the west side of South 18th

Change over traffic signals at 17th to new system

Two Week Look Ahead

UPDATED MARCH 30, 2017

PLEASE BE AWARE AND SHARE...

During the past week

Colored concrete is poured in medians from 22nd to 21st and from South 19th to North 19th

Pavement patching along new median curbs and temporary turn lane striping is complete

Turn lanes are open from 21st to North 19th

Roadway curbs and sidewalks are poured to the west entrance of McDonalds

Roadway curb and back curb on the west side of South 18th are poured to Moe's driveway

Old signal foundations removed and sidewalks re-poured at North 18th

- Silva cells at Firehouse are under construction

Over the next two weeks expect to see:

- Continue colored concrete in medians from 22nd to North 19th
- Begin installing irrigation and fiber reinforced planting soils in medians between 21st and South 19th
- Complete sidewalks on the west side of South 18th
- Complete duct bank installation along south side of Cumberland
- Complete electrical service conversions in South 19th as soon as junction box arrives

Two Week Look Ahead

UPDATED MARCH 23, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- Roadway curbs, sidewalks, and planter curbs are poured to the west radius at South 18th
- Sidewalks along the east side of South 18th are complete
- Furnishing zone construction complete to Wendy's
- Old signal foundations removed and sidewalks re-poured at 22nd and North 19th
- Median curbs are poured from 22nd to North 19th
- Silva cells are complete to McDonald's - four silva cells remain

Over the next two weeks expect to see:

- Begin pouring colored concrete in medians from 22nd to North 19th
- Patch asphalt in front of median curbs and stripe turn lanes from 22nd to North 19th
- Begin sidewalks on the west side of South 18th
- Complete duct bank installation along south side of Cumberland
- Complete electrical service conversions in South 19th as soon as junction box arrives

Two Week Look Ahead

March 16, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- All saw cutting for new medians from 22nd to North 19th is complete and removal of asphalt has progressed to North 20th
- All north side concrete has been poured through the first half of Wendy's driveway
- Sidewalks along the east side of South 18th have been poured
- Pavers installed to The 1830 Project

Over the next two weeks expect to see:

- Pour median curbs from 22nd to North 19th next week
- Begin pouring colored concrete in medians from 22nd to North 19th
- Complete furnishing zone construction across The 1830 Project
-

Complete duct bank installation along south side of Cumberland

Complete electrical service conversions in South 19th as soon as junction box arrives

Two Week Look Ahead

March 9, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- Paving thru binder on the east bound lane of Cumberland and all side streets from 22nd to east of North 19th is complete
- Sidewalks poured across The 1830 Project
- Pervious concrete is poured to half way across The 1830 Project
- South side electrical duct bank is installed to Melrose
- New signal system at the 18th Street intersection has been activated
- Pavers installed to Hannah's Cafe
- Silva cell installation at McDonald's is ongoing

Over the next two weeks expect to see:

- Begin median construction at 22nd and working east
- Continue furnishing zone construction across The 1830 Project
- Continue duct bank installation along south side of Cumberland
- Continue paver installation on south side of Cumberland across The 1830 Project
- Complete electrical service conversions in South 19th next week

Two Week Look Ahead

March 2, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- Full depth excavation of South 21st and Mountcastle is complete, South 19th ongoing
- Color concrete at all re-worked handicap ramps has been re-poured
- All concrete work in South 19th complete
- Flowable fill placed at back of sidewalk across The 1830 Project
- South side electrical duct bank is installed across Krystal's first driveway
- New signal system at the 18th Street intersection is complete
- Silva cell installation is complete to South 18th

Over the next two weeks expect to see:

- Paving the eastbound lane of Cumberland and south-side side streets today and tomorrow
- Continue sidewalks and furnishing zone construction across The 1830 Project
- Continue duct bank installation along south side of Cumberland
- Resume paver installation on south side of Cumberland from S19th heading east
- Complete electrical service conversions in South 19th next week

Two Week Look Ahead

February 23, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- Handicap ramps at South 21st and South 19th have been re-poured
- Catch basin installed in Taco Bell's parking lot and tied in to existing structure in South 19th
- Pervious Concrete is poured to The 1830 Project and ready for paver installation
- Roadway curb on Cumberland is poured to catch basin #33, just west of Wendy's
- Curbs on the east side of South 19th poured to the south alley
- Electrical duct bank work in South 18th complete
- Duct banks for electrical service conversion on the east side of South 19th are complete

Over the next two weeks expect to see:

- Begin sidewalks and furnishing zone construction across The 1830 Project
- Complete curbs and sidewalks in South 19th
- Pave the south lane of Cumberland and south-side side streets to full depth limits
- Complete electrical service conversions in South 19th
- Activate signal system at the 18th Street intersection

Two Week Look Ahead

February 16, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- Asphalt patching of south side driveways and alleys complete to North 19th
- Roadway curb, driveways, sidewalks, and planter curbs on Cumberland are complete to The 1830 Project
- Curbs on the east side of South 19th poured to the south alley
- Sidewalk panels and bench nook at Evolve have been re-poured
- Signal system at North 19th is active
- Signal poles at 18th have been installed
- Electrical service conversion to Taco Bell is complete, east side service conversions in South 19th are ongoing
- South side street lights are burning from Phase 1 to Zaxby's
- Pavers installed to Taco Bell

Over the next two weeks expect to see:

- Curbs and sidewalks across The 1830 Project
- Complete curbs and sidewalks in South 19th
- Continue silva cell installation to South 18th
- Complete electrical service conversions in South 19th

Two Week Look Ahead

February 9, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- Continue curbs and sidewalks in South 19th
- Complete furnishing zone construction from Mountcastle to South 19th
- Complete silva cells in front of 1830
- Complete paver installation from South 21st to Mountcastle
- Electrical duct banks from South 18th to end of project
- Activate new signal system at 19th

Over the next two weeks expect to see:

- Complete furnishing zone construction from Mountcastle to South 19th
- Complete curbs and sidewalks in South 19th
- Continue silva cells to South 18th
- Complete pave installation from Mountcastle to South 19th
- Electrical duct banks from South 18th to end of project

Two-Week Look Ahead

February 2, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- Roadway curb and sidewalks poured from 19th to The 1830 Project
- Curbs and sidewalks on the west side of South 19th
- Planter curbs poured to South 19th
- Signal system at North 19th is complete and awaiting inspections
- Electrical duct banks installed to McDonald's east entrance
- Electrical service conversions in South 19th are ongoing
- Silva cell excavation and installation in front of 1830
- Pavers installed to Evolve

Over the next two weeks expect to see:

- Complete furnishing zone construction from Mountcastle to South 19th
- Continue curbs and sidewalks in South 19th
- Complete silva cells in front of 1830
- Complete paver installation from South 21st to Mountcastle
- Electrical duct banks from South 18th to end of project
- Activate new signal system at 19th

Two-Week Look Ahead

January 26, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- Roadway curb and sidewalks poured to the radius at South 19th
- Planter curbs poured to Mountcastle
- Pervious concrete poured to Mountcastle
- Signal pole and arms installed at North 19th
- Traffic control cabinet pedestal poured for signals at North 19th
- Electrical duct banks on the south side of Cumberland installed across South 18th
- Silva cell excavation and installation in front of 1830

Pavers installed to Zaxby's

Over the next two weeks expect to see:

- Planter curbs and furnishing zone construction from Mountcastle to South 19th
- Excavate and install silva cells in front of 1830
- Paver installation from South 21st to Mountcastle
- Electrical duct banks from South 18th to end of project
- Activate new signal system at 19th

Two-Week Look Ahead

January 19, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- All storm drainage is installed!
- Roadway curb and sidewalks poured to Uptown Bar and Grille
- Signal pole foundation poured and signal infrastructure installed in from of 1830
- Electrical duct banks on the south side of Cumberland installed across 1830 to Wendy's
- Silva cell installation in front of Uptown Bar and Grille and Taco Bell is complete
- Pavers installed to mid-block between South 22nd and South 21st

Over the next two weeks expect to see:

- Continue curbs furnishing zone construction from South 21st to Mountcastle
- Excavate and install silva cells in front of 1830
- Continue south side paver installation
- Continue electrical duct banks on the south side of Cumberland

Two-Week Look Ahead

January 12, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- Final storm structure in Cumberland Avenue has been installed!
- Planter backfill and paver installation at 17th Street is complete
- North alley entrance off 18th Street at The Standard is complete
- Roadway curb and radius curb poured along east side of Mountcastle
- Sidewalks in front of Evolve have been poured
- Electrical duct banks on the south side of Cumberland installed to the 1830 project
- Silva cell installation in front of Uptown Bar and Grille and Taco Bell ongoing
- Pavers installed from Jason's Deli to Hype
- All north side street lights are now on line

Over the next two weeks expect to see:

- Complete storm drainage by pouring remaining inverts, setting remaining castings, and stalling area drain at Wendy's
- Continue curbs furnishing zone construction from South 21st to Mountcastle
- Complete silva cells up to South 19th
- Continue south side paver installation
- Continue electrical duct banks on the south side of Cumberland

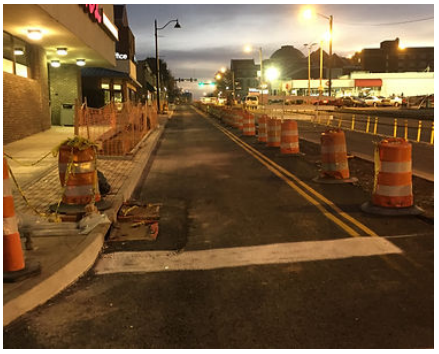

2017 IS HERE!!: Two-Week Look Ahead

January 5, 2017

PLEASE BE AWARE AND SHARE...

During the past week

- Planter rails have been removed until final installation in August 2017
- Planter curbs and pervious concrete between South 22nd and South 21st are complete
- Roadway curb poured at Panera
- Sidewalks between entrances of Zaxby's have been poured
- Electrical duct banks on the south side of Cumberland installed to Oscar's
- Lighting duct bank installed on the east side of South 19th
- Silva cells in front of Evolve are complete, sidewalks area graded and ready for concrete
- Excavation of silva sells in front of Uptown Bar and Grille and Taco Bell is complete
- South side storm drainage installed across 18th to storm structure 34B
- North alley entrance off 17th Street at The Standard has been poured
- Planter backfill and paver installation at 17th Street will be completed this week

Over the next two weeks expect to see:

- Complete south side storm drainage
- Continue curbs and sidewalks from South 21st to Mountcastle
- Complete silva cells up to South 19th
- Begin south side paver installation
- Street lighting and special events duct banks on the south side of Cumberland and begin electrical service conversions in South 19th

Happy New Year!: Two-Week Look Ahead

December 29, 2016

PLEASE BE AWARE AND SHARE...

During the past week

- South side roadway curb and back of sidewalk curb poured at Zaxby's
- Back sidewalk at east half of Zaxby's entrance poured
- Electrical duct banks on the south side of Cumberland to Long Branc
- Planter backfill and paver installation at 17th Street
- Silva cells in front of Evolve nearly complete

Over the next two weeks expect to see:

- No work on Monday 1/2/17
- Complete south side storm drainage
- Install pavers and backfill planters along Cumberland to endow project
- Planter curbs and pervious concrete from South 22nd to South 21st
- Continue curbs and sidewalks from South 21st to Mountcastle
- Street lighting and special events duct banks on the south side of Cumberland and electrical service conversions in South 19th

Merry Christmas!: Two-Week Look Ahead

December 22, 2016

PLEASE BE AWARE AND SHARE...

During the past week

-

- Trolley track removal is now complete.
- 17th intersection rebuild is complete.
- Storm installed to structure 34A and ready to cross South 18th next week
- Sidewalks at Sunspot are poured.
- South side sidewalks have been poured to South 21st
- Sidewalks on the west side of South 21st have been poured
- Electrical duct banks on the south side of Cumberland installed to Uptown Bar & Grill
- Planters back fill and paver installation along east side of 17th have been completed
- Silva cells in front of Evolve nearly complete

Over the next two weeks expect to see:

- No work on Monday 12/26/2016
- Continue south side storm drainage
- Install pavers and backfill planters along Cumberland to end of project
- Planter curbs from South 22nd to South 21st
- Begin curbs and sidewalks from South 21st to Mountcastle
- Street lighting and special events duct banks on the south side of Cumberland and electrical service conversions in South 19th

SPECIAL UPDATE: Two-Week Look Ahead

December 15, 2016

PLEASE BE AWARE AND SHARE...

INTERSECTION REBUILD TO CLOSE CUMBERLAND AVENUE AT 17TH STREET - read full press release...

During the past week

- Storm installed to structure #33 42" reinforced concrete pipe storm drainage is complete.
- All sidewalks, handicap landings, and planter curbs have been poured along 17th and Cumberland
- Sidewalks have been poured from the radius at South 22nd to the entrance to Hype Energy
- Radius curbs on the west side of South 21st are complete
- Entrance to Subway from South 21st has been poured
- Electrical duct banks on the south side of Cumberland installed across Mountcastle

Over the next two weeks expect to see:

- 17th Street intersection rebuild scheduled to begin at 10pm, Thursday, December 15 through 6am Monday, December 19
- Continue south side storm drainage
- Install pavers and backfill planters on the east side of 17th and along Cumberland
- Silva cell installation at Evolve
- South Side roadway curb and sidewalks from South 22nd to South 21st as temperatures allow
- Complete curbs and sidewalks in South 21st
- Street lighting and special events duct banks on the south side of Cumberland

Two-Week Look Ahead

DECEMBER 8, 2016

During the past week

- Signal system at South 22nd is active and the old signal equipment removed
- Trolley track removed from North 19th to 17th, and center lane repaved
- Storm structure installed and tied in the 36" RCP from north side

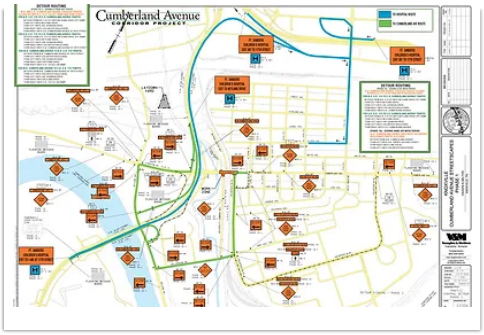

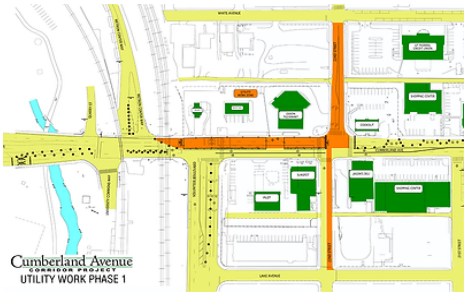

- Full depth rebuild of North 21st to the North alley completed and repaved
- Sidewalks along 17th and Cumberland have been pounded, only handicap landings and planter curbs remain
- Roadway curbs on the west side of South 21st are complete
- Entrance to Subway from South 21st poured
- Electrical duct banks only south side of Cumberland have progressed to Mountcastle

Over the next two weeks expect to see:

- Continue South side storm drainage
- Install pavers on the east side of 17th
- Continue silva cell installation at Evolve
- Continue south side roadway curb and sidewalks from South 22nd to South 21st
- Continue curbs and sidewalks on west side of South 21st
- Continue street lighting and special events duct banks on the south side of Cumberland
- 17th Street intersection rebuild - 24/7 work

Two-Week Look Ahead

DECEMBER 1, 2016

PLEASE BE AWARE AND SHARE...

Due to rainy weather conditions, 24/7 night time work has been extended through Thursday, December 1, work will continue over night Thursday into Friday morning. No overnight work will occur tonight, Wednesday, because of wet conditions. Only day time work will occur during final exams, which start on Saturday.

On Monday November 21 westbound traffic was shifted to the north side of Cumberland Avenue between 19th Street and 17th Street for the removal of the remaining trolley track located in the middle of the roadway.

During this week, construction crews cut and began the hammering of the asphalt and concrete around the trolley tracks during day time hours.

On Sunday, November 27 the 24/7 work began to complete the trolley track removal, however, wind and rain on both Monday and Tuesday nights limited the amount of work that could be completed.

No left turns will be allowed between 17th and North 19th streets during the track removal.

All paving work will be complete and left turns at North 19th and 18th will be restored by the morning of Thursday, December 8 prior to graduation ceremonies.

During the past week

- Signal system at South 22nd installed and will be activated Friday, December 2 at 9:00am
- All north side street lights are burning up to Goodwill on 17th
- Sidewalks in front of Panda Express/Raising Cane's are poure
- Roadway curb on 17th is poured
- Entrance to Clement Hall loading area on 17th and sidewalks north of the entrance are poured
- Trolley track removals from North 19 to 17th will be completed Thursday, December 1
- Electrical duct banks on the south side of Cumberland have progressed to Evolve
- Silva cells installed to Evolve on the south side, north side Silva cells are complete

Paver installation on north side in complete to the north alley on the west side of 17th

- Roadway curb on the south side of Cumberland poured to just west of South 21st

Over the next two weeks expect to see:

- Pave center lane of Cumberland and North 21st tomorrow and Saturday
- Complete curbs and sidewalks on the east side of 17th
- Begin silva cell installation at Evolve
- Continue south side roadway curb and sidewalks from South 22nd to South 21st
- Continue curbs and sidewalks in South 21st
- Continue street lighting and special events duct banks on the south side of Cumberland
- 17th Street intersection rebuild

SPECIAL UPDATE: Two-Week Look Ahead

November 30, 2016

PLEASE BE AWARE AND SHARE...

Due to rainy weather conditions, 24/7 night time work has been extended through Thursday, December 1, work will continue over night Thursday into Friday morning. No overnight work will occur tonight, Wednesday, because of wet conditions. Only day time work will occur during final exams, which start on Saturday.

On Monday November 21 westbound traffic was shifted to the north side of Cumberland Avenue between 19th Street and 17th Street for the removal of the remaining trolley track located in the middle of the roadway.

During this week, construction crews cut and began the hammering of the asphalt and concrete around the trolley tracks during day time hours.

On Sunday, November 27 the 24/7 work began to complete the trolley track removal, however, wind and rain on both Monday and Tuesday nights limited the amount of work that could be completed.

No left turns will be allowed between 17th and North 19th streets during the track removal.

All paving work will be complete and left turns at North 19th and 18th will be restored by the morning of Thursday, December 8 prior to graduation ceremonies.

During the past week

- Signal poles at South 22nd installed and signal wiring pulled
- Lighting control center #2 installed along with street light poles up to Goodwill
- Electrical duct banks in South 21st are complete
- Electrical duct banks on the south side of Cumberland are installed to the eastern entrance to Zaxbys
- Silva cells installed to South 21st on the south side.
- North side Silva cells are complete
- Paver installation on north side is up to the north alley on the west side of 17th
-

42" storm installed to structure 31 at Longbranch (just west of North 19th)

- Roadway curb on the south side of Cumberland poured from through the entrance to Hype Energy location
- Entrance to Hype Energy has been poured
- Sidewalks in front of Panda Express/Raising Cane's will be poured by end of day 11/17/2016.

Over the next two weeks expect to see:

- Continue curbs and sidewalks on the east side of 17th
- South side roadway curb and sidewalks from South 22nd to South 21st
- Continue curbs and sidewalks in South 21st
- Trolley track excavation and center lane construction from North 19th to 17th
- Continue street lighting and special events duct banks on the south side of Cumberland
- Traffic signals at 22nd should be active by the end of November pending COK inspection
- Street lights along the north side will be burning by the end of November

Two-Week Look Ahead

November 10, 2016

During the past week

- Electrical duct banks installed across South 21st on south side
- Electrical duct banks on North side of Cumberland completed
- Silva cells at Jason's Deli installed on south side
- Pave installation on north side is up to 17th
- 42" storm installed across South 19th
- Roadway curb on Cumberland poured from end of project back to Raising Cane's
- Curbs and sidewalks along the west side of South 21st complete from South alley to Subway entrance

Over the next two weeks expect to see:

- Complete pavers on north side from 19th to 17th
- Begin curbs and sidewalks on the east side of 17th
- Continue curbs and sidewalks in South 21st
- Continue storm drainage on south side of Cumberland
- Continue street lighting and special events duct banks on the south side of Cumberland

Two-Week Look Ahead

November 3, 2016

During the past week

- Electrical duct banks installed to South 21st
- Paver installation at Beat the Bookstore and progressing towards 17th
- Type B planters at Regions Bank and Niro's Gyros have been rebuilt
- Extended curbs on Shell Station property have been poured
- Sidewalks on the east side of North 19th complete
- 42" storm installed to just east of Panera Bread
- Asphalt patching along curb lines in North 18th and North 19th

Over the next two weeks expect to see:

- Continue paver installation on north side from 19th to 17th
- Begin curbs and sidewalks on the east side of 17th
- Continue curbs and sidewalks in South 21st
- Shift traffic 11/28/2016 to begin center lane excavation from west of North 19th to the end of the project (just past 17th)
- Continue storm drainage on south side of Cumberland
- Continue street lighting and special events duct banks on the south side of Cumberland

Two-Week Look Ahead

October 25, 2016

During the past week

- North side lighting is active to The House of Dragon
- North 20th rebuilt and paved thru binder up to the North Alley
- Westbound land of Cumberland rebuilt and paved thru binder from North 19th to 17th
- Electrical duct banks installed from the end of the project back to 17th on the north side and up to Hype Energy on the south side
- Radius curbs on the east and west sides of South 22nd
- Roadway curb from the end of the project back to the Vol Shop
- Sidewalks on the east side of North 19th to the Region Bank drive thru exit
- 42" storm installed to Mountcastle Street

Over the next two weeks expect to see:

- B planter rebuild at Regions Bank and Niro's Gyros
- Pavers to be installed on north side from 19th to 17th
- Curbs and sidewalks on the east side of 17th
- Complete sidewalks on the east side of North 19th
- Complete Phase 1 sidewalks on South 22nd
- Continue storm drainage on south side of Cumberland
- Continue street lighting and special events duct banks on the south side of Cumberland

Two-Week Look Ahead

October 20, 2016

During the past week

- Street lighting duct bank from the end of the project working back towards 17th
- Signal system infrastructure for the south side of 22nd
- Planter curbs on the west side of 17th
- Planter curbs 1700 block
- Roadway curb on the east side of South 22nd
- Roadway curb on the east side of North 19th
- 42" storm installed to Evolve
- Full depth rebuild of future westbound lane from 19th to 17th is ready for paving

Over the next two weeks expect to see:

- Pave the new westbound lane through binder from east of 19th to west of 17th
- Pave North 20th, North 18th, and potentially North 21st through binder
- Curbs and sidewalks on the east side of 17th
- Complete sidewalks on the east side of North 19th
- Complete sidewalks on South 22nd
- Continue storm drainage on south side of Cumberland
- Continue street lighting and special events duct banks on the south side of Cumberland
- Power on new street lights on the north side of Cumberland to North 19th

Two-Week Look Ahead

October 13, 2016

PLEASE BE AWARE AND SHARE...

South 22nd Street will be closed through October 15 to install 42" storm line across South 22nd. The right southbound lane of 17th Street will be closed through October 14 to build roadway curb, furnishing zone and sidewalks.

During the past week

- 42" Storm installed to the west side of the South 21st intersection
- Full depth rebuild of the 22nd Street intersection is complete
- Full depth rebuild of future westbound land from 19th to 18th
- Sidewalks east side of North 18th are complete
- Sidewalks on Cumberland will be complete from Tyson Park all the way to the north alley on 17th Street
- Signals at 17th and White and at 17th and Clinch are operational

Over the next two weeks expect to see:

- Complete planter curbs in 1700 block
- Complete planter curbs on the west side of 17th
- Begin curbs and sidewalks on the east side of 17th
- Begin sidewalks on the east side of North 19th
- Complete sidewalks on South 22nd
- Continue storm drainage on south side of Cumberland
- Continue street lighting and special events duct banks on the south side of Cumberland
- Complete full depth rebuild of future westbound lane of Cumberland and pave from 19th to 17th

Two-Week Look Ahead

October 6, 2016

PLEASE BE AWARE AND SHARE...

South 22nd Street will be closed through October 15 to install 42" storm line across South 22nd. The right southbound lane of 17th Street will be closed through October 14 to build roadway curb, furnishing zone and sidewalks.

During the past week

- 42" Storm installed to catch basin #25
- Full depth excavation of North 22nd completed. Base stone to be placed today. Paving to start tonight
- Sidewalks and alley entrance West of North 18th completed
- Sidewalks on Cumberland poured to entrance of Brenz Pizza
- Planter curbs done at Goodwill
- Planter rails installed to North 18th

Signals at 17th/White and 17th/Clinch will be activated today

Over the next two weeks expect to see:

- Complete curbs and sidewalks in 1700 block
- Complete curbs and sidewalks on east side of 17th
- Complete curbs and sidewalks on the east side of North 18th
- Continue storm drainage on south side of Cumberland
- Continue street lighting and special events duct banks on the south side of Cumberland

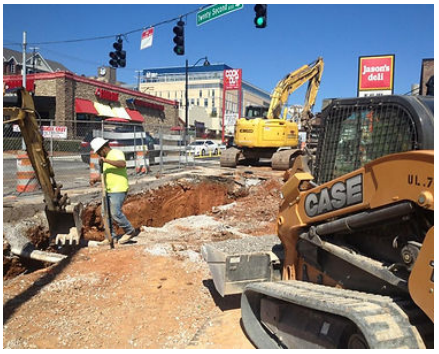

Two-Week Look Ahead

September 29, 2016

PLEASE BE AWARE AND SHARE...

South 22nd Street will be closed through October 15 to install 42" storm line across South 22nd. The right southbound lane of 17th Street will be closed through October 14 to build roadway curb, furnishing zone and sidewalks.

During the past week

- 42" storm installed through the east entrance to Hype Energy
- Pavers are installed to the west corner of North 18th
- Roadway curb on the west side on North 18th poured from the corner through the alley
- Roadway curb on the north side of Cumberland complete to the corner of 17th
- Planter curbs at Walgreens and Fedex/Kinkos
- Sidewalks on Cumberland poured to Beat the Bookstore
- Sidewalks on the west side of 17th have been poured from the North alley to Fort Sanders Yacht Club
- Radius curb and sidewalks on the NW and SW corners of 22nd
- Planter rails complete to Tin Roof

Over the next two weeks expect to see:

- Continue curbs and sidewalks in 1700 block
- Continue curbs and sidewalks on east side of 17th
- Begin curbs and sidewalks on the west side of North 18th
- Continue storm drainage on south side of Cumberland
- Continue street lighting and special events duct banks on the south side of Cumberland
- Signals at 17th and White and 17th and Clinch will be activated next week once signal timing is provided
- Left turn signal for EB traffic at North 19th will be will be activated during the rebuild of the 22nd intersection once signal timing is provided

Two-Week Look Ahead

September 22, 2016

PLEASE BE AWARE AND SHARE...

Traffic has been shifted to place both eastbound and westbound traffic against the new north side curb line

from west of North 19th to 22nd. There will be a four-week closure of the right southbound lane of 17th Street (began Monday 9/12/2016) to build roadway curb, furnishing zone and sidewalks. South 22nd Street will be closed the week of September 19 to install 42" storm line across South 22nd.

During the past week

- 42" storm lin installed through South 22nd intersection to catch basin 24 (near Sunspot)
- Pavers are installed to Copper Cellar
- Sidewalks on Cumberland are poured through western half of Walgreens entrance
- Sidewalk portion of the entrance to the vacant lot east of Fedex/Kinkos has been poured
- Sidewalks on the west side of 17th have been poured from the North alley to just south of Goodwill's door
- Combined curb and sidewalk beyond the ROW at 2121 Cumberland (Insomnia Cookies)
- North side silva cells complete to the west corner of 17th
- Type B planter rails installed at Cookout and Mellow Mushroom

Over the next two weeks expect to see:

- Continue curbs and sidewalks in 1700 block
- Continue curbs and sidewalks on east side of 17th
- Begin curbs and sidewalks on the west side of North 18th
- Construct curbs and sidewalk on the NW and SW corners of 22nd
- Continue storm rainage on south side of Cumberland
- Continue street lighting and special events duct banks on the south side of Cumberland
- Signals at 17th and White and 17th and Clinch will be activated next week once signal timing is provided
- Left turn signal for EB traffic at north 19th will be installed next week, signal will be activated during the rebuild of the 22nd intersection once signal timing is provided

Two-Week Look Ahead

September 15, 2016

PLEASE BE AWARE AND SHARE...

Traffic has been shifted to place both eastbound and westbound traffic against the new north side curb line from west of North 19th to 22nd. Left turn lanes from 22nd to North 19th have been re-established.

There will be a four-week closure of the right southbound lane of 17th Street (began MOnday 9/12/2016) to build roadway curb, furnishing zone and sidewalks.

South 22nd Street will be closed the week of September 19 to install 42" storm line across South 22nd.

During the past week

- Trolley track removal and excavation to subgrade for center land completed from 22nd to North 19th
- Catch basin #67 installed in North 18th, north side storm drainage is now complete
- Base stone placement in center lane complete form 22nd to North 19th
- Pavement through binder in center lane complete from 22nd to North 19th
- Roadway curb and sidewalks on east side of North 21st are complete
- Signal pole arm installed at the corner of 17th and White
- Pavers are installed to Hibachi Factory
- Roadway curb poured east to Beat the Bookstore
- Roadway curb poured along the east side of 17th
- Completing silva cells at Brenz Pizza and Chipotle

Over the next two weeks expect to see:

- Continue curbs and sidewalks in 1700 block
- Continue curbs and sidewalks on east side of 17th
- Begin storm drainage on south side of Cumberland starting at South 22nd
- Begin street lighting and special events duct banks on the south side of Cumberland

Two-Week Look Ahead

September 8, 2016

PLEASE BE AWARE AND SHARE...

During the week of September 5, 2016 ending Friday, September 16 there will be a 24/7 operation to remove trolley track from 22nd to 19th. Traffic pattern will change this week.

During the past week

- Trolley track removal and excavation to subgrade for center land complete from 22nd through North 20th
- Base stone placement beginning today at 22nd working east
- Pavers are installed to Niro's Gyros
- Roadway curb on the east side of North 21st are poured
- Sidewalks on the east side of North 21st are poured
- Adjusting existing storm structure north of Starbucks on North 21st today (9/8/2016)
- Sidewalks poured from corner of 18th to Walgreen's doorway
- Installing silva cells at Brenz Pizza

Over the next two weeks expect to see:

- Continue curbs and sidewalks in 1700 block
- Complete silva cell installation in the 1700 block
- Complete 24/7 operation to remove trolley track from 22nd to 19th
- Paving center lane from 22nd to 19th scheduled to begin 9/12/2016
- Install catch basin 67 (near old McAlisters building) in North 18th at the north alley

Two-Week Look Ahead

September 1, 2016

PLEASE BE AWARE AND SHARE...

During the week of September 5, 2016 there will be a 24/7 operation to remove trolley track from 22nd to 19th. Traffic pattern will change this week.

During the past week

- North sidewalks are complete to North 18th
- Repair of type B planters at Studio X in complete
- Roadway curbs and sidewalks on both sides of North 20th are complete
- Roadway curb and sidewalks on the west side of North 21st are complete
- Starbucks drive thru is complete and open to traffic
- Roadway curb on the east side of North 21st is complete to Starbucks entrance
- Street light poles and luminaires installed to Hibachi Factory

Over the next two weeks expect to see:

- Complete curb and sidewalk construction on east side of North 21st
- Continue curb and sidewalk construction in North 19th
- Continue curbs and sidewalks in 1700 block
- Continue silva cell installation in the 1700 block
- 24/7 operation to remove trolley track from 22nd to 19th week of 9/5/2016
- Paving from 22nd to 19th scheduled to begin 9/12/2016
- Install catch basin 67 in North 18th at the north alley

Two-Week Look Ahead

August 25, 2016

PLEASE BE AWARE AND SHARE...

During the past week

- Repair of type B planters at Mellow Mushroom and Cookout are complete
- Repair of type B planters at Tin Roof and House of Dragon poured this morning
- All colored and pervious concrete has been poured to the radius at North 18th
- Roadway curb and sidewalks on west side of North 19th are complete
- Roadway curb and sidewalks east side of North 20th will be complete this week
- Roadway curb on the west side on North 21st will be poured today (Thursday, August 25)
- Pavers installed to North 19th
- Signal system foundations at North 18th are complete
- Installation of street light poles and luminaires from 22nd to North 19th ongoing
- Utility poles removed on North 20th and 17th

Over the next two weeks expect to see:

- Complete curb and sidewalk construction in North 21st
- Complete curb and sidewalk construction in North 20th
- Continue curb and sidewalk construction in North 19th
- Continue curb and sidewalks in 1700 block
- Continue silva cell installation in the 1700 block

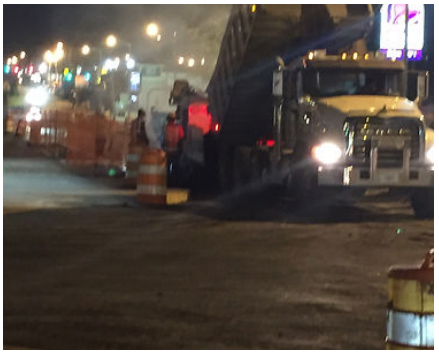

Two-Week Look Ahead

August 18, 2016

PLEASE BE AWARE AND SHARE...

During the past week

- Storm Line in North 18th Street installed
- Repair planter at Shell completed
- Repair planter at Cook Out and Mellow Mushroom formed for pouring
- Sidewalks and planter curbs poured at North 18th Street
- Roadway curb in Cumberland poured to east side of Walgreens
- Roadway curb on west side of North 19th poured, with sidewalk poured as weather permits
- Roadway curb on east side of North 20th formed, will pour as weather permits
- Tree guard/planter rails installed to North 19th Street

Over the next two weeks expect to see:

- Continue curb and sidewalk construction in North 19th
- Continue curb and sidewalk consrtuction in North 20th
- Begin curb and sidewalk construction in North 21st
- Complete sidewalks and planter curbs in the 1800 block
- Continue curbs and sidewalks in 1700 block
- Continue silva call installation in the 1700 block

Two-Week Look Ahead

August 11, 2016

PLEASE BE AWARE AND SHARE...

During the past week

- Demobilizing and removing lane restrictions in Cumberland at 16th and Volunteer
- Utility upgrades have been completed!
- New future westbound lane of Cumberland paved from 22nd to 19th
- Storm water line M completed in North 18th
- Roof drains at Stefano's and Piano Bar/Future 1st TN Bank have been installed
- Planter repairs have been made at the Shell station
- Planter curbs poured to east of Copper Cellar
- Electrical duct bank installed across Cumberland at 17th

Planters and passive irrigation installation completed at Walgreens and Fedex/Kinkos

Over the next two weeks expect to see:

- Curb and sidewalk construction in North 19th
- Complete sidewalks and planter curbs in th 1800 block
- Begin Curbs and sidewalks in 1700 block
- Continue silva cell installation in the 1700 block
- Storm line M in North 18th

Two-Week Look Ahead

August 4, 2016

PLEASE BE AWARE AND SHARE...

During the past week

- Demobilizing and removing lane restrictions in Cumberland at 16th and Volunteer
- Substantial completion has been achieved on the Utility upgrades. All new utilities are tested and in service
- Roadway excavation nd base stone is complet to east of North 19th
- New future westbound lane of Cumberland paved from western Shell entrance to South 22nd
- Sidewalks from back of ROW to edge of buildings, between Regions Bank and Copper Cellar
- Electrical duct bank installed in South 21st
- Silva cell installation has progressed to Fedex/Kinkos

Over the next two weeks expect to see:

- Continue paving operation of future westbound lane tonight (Thursday, August 4) and Friday, August 5 ending just east of North 19th
- Begin curb and sidewalk construction in North 19th
- Complete sidewalks and planter curbs in the 1800 block
- Continue silva cell installation in the 1700 block
- Install planter rails in planters from 22nd and 20th
- Storm line M in North 18th

Two-Week Look Ahead

July 28, 2016

PLEASE BE AWARE AND SHARE...

During the past week

- Attemp to tie the water main in Cumberland at Volunteer is shceduled for Thursday, July 28.
- Water line L in Melrose has been tied in at Lake Avenue
- Domestic service and fire line to Baker Center has been tied in
- Fire line to Cane's Chicken has been tied in
- Roadway excavation has progressed east of North 19th
- Base stone installed to North 19th

- Sidewalks complete to Copper Cellar
- Electrical duct bank installed to to 17th and halfway across Cumberland at 17th
- Northside overhead electrical removals complete

Over the next two weeks expect to see:

- Repave intersection of Cumberland and 16th and shift traffic back to the south side of Cumberland west of the intersection
- Connect UT Henson Hall to new main
- Water line M in 17th tied in at White
- Paving rescheduled to begin August 1 starting at 22nd and proceeding east to North 19th during this mobilization
- Sidewalks from back of ROW to edge of buildings, between Regions Bank and Copper Cellar
- Continue sidewalks and planter curbs in the 1800 block
- Continue silva cell installation in the 1700 block
- Install planter rails in planters from 22nd and 20th
- Storm line M in North 18th

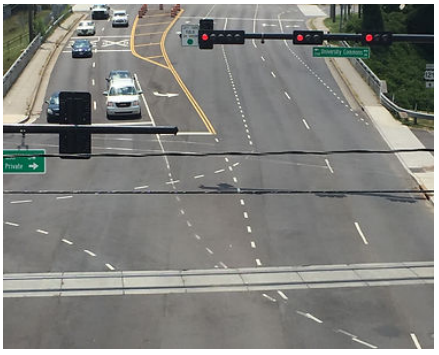

Two-Week Look Ahead

July 21, 2016

PLEASE BE AWARE AND SHARE...

During the past week

- Water line L in Melrose tested and ready for final connections
- Gas main in Cumberland tested and tied in to existing factilities in Volunteer completing the gas main portion of the project
- Water main in Cumberland installed to end of project, tested and will be tied in to existing facilities on Thursday, July 22.
- Roadway excavation has progressed east of North 20th
- Base stone installed to North 20th
- Roadway curbs poured to corner of North 18th at Copper Cellar
- Radius on east side of North 19th has been poured
- Pervious pavers installed to Jimmy John's
- Electrical duct bank installed to Chipotle
- Overhead electrical wiring removals complete to 17th

Over the next two weeks expect to see:

- Repave intersection of Cumberland and 16th and shift traffic back to the south side of Cumberland west of the intersection
- Connect UT Baker Center and UT Henson Hall to new main
- Tie in water line L in Melrose at Lake Avenue
- Tie in water line M in 17th at White
- Continue roadway grading for the new westbound lanes progressing east
- Continue sidewalks and planter curbs in the 1800 block
- Remove remaining north side overhead electrical
- Begin silva cell installation in the 1700 block
- Paving rescheduled to begin August 1 starting at 22nd and proceeding east to North 19th during this mobilization

Two-Week Look Ahead

July 14, 2016

PLEASE BE AWARE AND SHARE...

During the past week

- Clement Hall water and fire lines have been connected to new main
- Fire hydrant service installed across Melrose
- Water line L in Melrose has been installed and undergoing testing
- Water main and gas mains in Cumberland installed to end of project and undergoing testing
- Additional sourth side temporary lighting installed
- Electrical service conversions in 17th Street (at Goodwill and Cain's Chicken) are complete
- Roadway excavation has progressed from 22nd to 21st
- Planter curbs poured at Regions Bank
- Sidewalks poured adjacent to Copper Cellar entrance
- Pavers installed to University Liquors
- Pervious concrete poured to North 19th
- Electrical duct bank installed to Smoke Rings

Over the next two weeks expect to see:

- Connect new water and gas mains to existing lines in Cumberland at East Volunteer, closure of the intersection will not be necessary
- Connect UT Baker Center and UT Henson Hall to new main after testing in complete
- Tie in water line M in 17th at White
- Tie in water line L in Melrose at Lake
- Continue roadway grading for the new westbound lanes progressing east
- Continue sidewalks and planter curbs in the 1800 block
- Remove remaining north side overhead electrical
- Begin silva cell installation in the 1700 block
- Paving scheduled to begin 7/25 starting at 22nd

Two-Week Look Ahead

July 7, 2016

PLEASE BE AWARE AND SHARE...

Special work is being performed for the University for Tennessee new steam line across Cumberland Avenue at 16th Street. **East bound left turns will not be allowed through Wednesday, July 13.** Traffic can access east bound left turns at James Agee Street and 11th Street - left turns will not be allowed at Volunteer Blvd. and 16th Street through July 13.

During the past week

- Installed water main and and service connections in 18th North
- Completed water main connection across Cumberland at 18th
- Install water main and gas main from 17th working east to end of project
-

Storm drainage in North 18th encountered conflict with elecrical duct bank at the north alley

- Sidewalks and planter curbs poured to Regions Bank
- Electrical duct bank installed to gravel laydown yard used by The Standard
- Paver installation progressed to University Liquors

Over the next two weeks expect to see:

- Continue water and gas main in Cumberland from 17th to 16th
- Complete water line L in Melrose
- Overnight closure of Melrose to install fire hydrant across road
- One night closure of 16th and Cumberland intersection the week of July 18, 2016
- Begin trolley track removal and grading the new westbound lanes starting at 22nd and progessing eastward
- Complete electrical service converstions in 17th Street once power is available from transformers at The Standard
- Complete pouring sidewalks and planter curbs in the 1900 block
- Continue working on sidewalks and planter curbs in the 1800 block
- Install south side temporary lighting east of 18th
- Remove remaining north side overhead eletrical
- Begin silva cell installation in the 1700 block (once overhead electrical is removed)

Two-Week Look Ahead

June 30, 2016

PLEASE BE AWARE AND SHARE...

Special work is being performed for the University for Tennessee new steam line across Cumberland Avenue at 16th Street. **East bound left turns will not be allowed through Wednesday, July 13.** Traffic can access east bound left turns at James Agee Street and 11th Street - left turns will not be allowed at Volunteer Blvd. and 16th Street from June 23 through July 13.

During the past week

- Insert-a-valve has been installed on existing water main in Melrose
- Completed water service connections in 18th South
- Completed water service connections on Cumberland from 18th to 17th
- Installed water main and gas main from 17th working east to end of project
- Asphalt patching of 19th from alley to Cumberland
- Asphalt patching of entrances to Mellow Mushroom, Copper Cellar and Regions Bank
- Asphalt patching of 17th from alley to Cumberland
- Sidewalks and planter curbs poured to the former Piano Bar location
- Entrance to Copper Cellar re-opened with new driveway
- Electrical duct bank installed to west side of FedEx Kinkos
- Silva Cells installed to 18th
- Planter rail installed in first planter at Cook Out - awaiting review

Over the next two weeks expect to see:

- Continue water and gas main in Cumberland from 17th to 16th
- Complete water line L in Melrose
- Closure of Melrose to instll fire hydrant across road
- Complete storm drainage in 18th (delayed by rock excavation)
- Complete electrical service conversions in 17th Street once power is available from transformers at The Stanard
- Complete pouring sidewalks and planter curbs in the 1900 block
- Begin sidewalks in 1800 block

- Install south side temporary lighting east of 18th
- Remove remaining north side overhead electrical
- Complete silva cell installation in the 1700 block

Two-Week Look Ahead

June 23, 2016

PLEASE BE AWARE AND SHARE...

Special work is being performed for the University for Tennessee new steam line across Cumberland Avenue at 16th Street. East bound left turns will not be allowed through Wednesday, July 13. Traffic can access east bound left turns at James Agee Street and 11th Street - left turns will not be allowed at Volunteer Blvd. and 16th Street from June 23 through July 13..

During the past week

- Insert-a-valve has been installed on existing water mains in Cumberland at 16th
- The fire hydrant has been raised at the corner of Cumberland an 20th
- Water lines have been tested in 17th, South 18th and in Cumberland between 18th and 17th
- Installed water main and gas ain from 17th working east to end of project
- Storm drainage in 19th is complete
- Roadway curb poured to Copper Cellar
- Sidewalks and planter curbs poured to Jimmy Johns
- The new driveway is being poured at Copper Cellar and will be completed by Monday, June 27
- Paver installation has progressed to 20th
- Electrical duct bank installed to east side of Kinkos

Over the next two weeks expect to see:

- Continue water and gas main in Cumberland from 17th to 16th
- Complete water services on Cumberland from 18th to 17th
- Insert-a-valve and tie in for water line L in Melrose

  NOTE: Insert-a-valves are shutoff values added to water lines that allow for future work to be performed with minimal or no disruption of services.
- There will be an overnight closure of Cumberland to connect water line in South 18th to the main in Cumberland beginning Monday, June 27
- Complete storm drainage in 18th (currently hammering rock)
- Complete electrical service conversions in 17th Street once power is available from transformers at The Stanard
- Complete pervious paver installation in the 1900 block

  NOTE: Pervious pavers allow stormwater to percolate through the surface rather than running off into surrounding areas or storm drains. As water runs through, the pavers filter urban pollutants. Like grass, pervious pavers let the ground below breathe. These pavers also allow tree roots and their supporting microbes to interact. (Source: Water Environment Federation, 2013).
- Complete pouring sidewalks and planter curbs in the 1900 block
- Begin sidewalks in 1800 block
- Install south side temporary lighting east of 18th
- Remove remaining north side overhead electrical
- Complete silva cell installation in the 1700 block

Two-Week Look Ahead

June 16, 2016

PLEASE BE AWARE AND SHARE...

Special work is being performed for the University for Tennessee new steam line across Cumberland Avenue at 16th Street. East bound left turns will not be allowed through Wednesday, July 13. Traffic can access east bound left turns at James Agee Street and 11th Street - west bound left turn at Volunteer is accessible through June 17.

During the past week

- Began installation of waterline L in Melrose
- The water line has been tied in at South 18th and Lake Avenue
- Fire line to Walgreens has been tied to the new main at 18th
- Traffic shift and barrier rail in place between 17th and 16th
- Storm drainage in 17th is complete
- Storm drainage in 19th will be complete by Friday, June 17
- Roadway curb poured to 1821 Cumberland
- Sidewalks poured to mid-block between 20th and 19th
- Paver installation has progressed to midway through 2000 block
- Pedestrian corsswalks have been re-marked at 22nd, 21st and 20th
- Electrical duct bank has been installed to FedEx Kinkos driveway

Over the next two weeks expect to see:

- Install Insert-a-valve on existing water mains in Cumberland at 16th on June 16
  NOTE: Insert-a-valves are shutoff values added to water lines that allow for future work to be performed with minimal or no disruption of services.
- Complete water line L in Melrose
- Install water and gas main in Cumberland from 17th to 16th
- Connect service lines in 17th to new main
- Connect water services on Cumberland from 18th to 17th
- Overnight closure to connect water line in South 18th to the main in Cumberland
- Install storm drainage in North 18th
- Complete electrical service conversions in 17th Street once power is available from transformers at The Standard
- Complete pervious paver installation in the 2000 block
  NOTE: Pervious pavers allow stormwater to percolate through the surface rather than running off into surrounding areas or storm drains. As water runs through, the pavers filter urban pollutants. Like grass, pervious pavers let the ground below breathe. These pavers also allow tree roots and their supporting microbes to interact. (Source: Water Environment Federation, 2013).
- Complete pouring sidewalks and planter curbs in the 1900 block
- Complete silva cell installation in the 1800 block

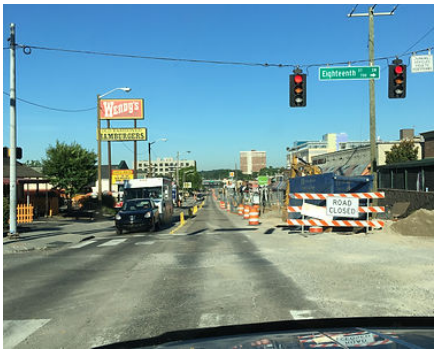

Two-Week Look Ahead

June 9, 2016

PLEASE BE AWARE AND SHARE...

Special work is being performed for the University for Tennessee new steam line across Cumberland Avenue at 16th Street. East bound left turns will not be allowed through Wednesday, July 13. Traffic can access east bound left turns at James Agee Street and 11th Street - west bound left turn at Volunteer is accessible through June 17.

During the past week

- Insert-a-valves installed in North 19th and 17th
  NOTE: Insert-a-valves are shutoff values added to water lines that allow for future work to be performed with minimal or no disruption of services.
- Fire line to Copper Cellar has been tied to the new main
- Storm drainage installed in 17th from structures 43 to 44, 44 to 45 and 45 to 46
- Tree well and Silva cell excavation has progressed to North 18th
- Roadway curbs have been poured to Half Barrel
- Entrance to Regions Bank has been poured

Sidewalks poured next to Jimmy Johns

Paver installation in ongoing in 2000 block

Over the next two weeks expect to see:

Install water line L in Melrose

Overnight closure to connect water line in South 18th to the main in Cumberland

Install insert-a-valves on existing water mains in Cumberland at 16th

Traffic shift between 17th and 16th to install final runs of water and gas to the end of project

Overnight closure to connect water line in South 18th to the main in Cumberland

Complete storm drainage in 17th and North 19th

Install storm drainage in North 18th

Continue electrical service conversions in 17th Street

Continue pervious pavers in the 2000 block

> NOTE: Pervious pavers allow stormwater to percolate through the surface rather than running off into surrounding areas or storm drains. As water runs through, the pavers filter urban pollutants. Like grass, pervious pavers let the ground below breathe. These pavers also allow tree roots and their supporting microbes to interact. (Source: Water Environment Federation, 2013).

Continue pouring sidewalks and planters in the 1900 block

Continue silva cell installation in the 1800 block

Two-Week Look Ahead

June 2, 2016

PLEASE BE AWARE AND SHARE...

During the past week

Sewer work in south alley completed and alley repaved

Water line K (near Walgreens) installed in North 18th

North alley between 18th and 19th has been repaved

Business entrances from 22nd to 19th have been repaved

Storm drainage in Cumberland installed to 17th

Street light poles installed to 20th

Tree well Silva cell excavation has progressed to Copper Cellar

Sidewalks poured to University Liquors

Paver installation in ongoing in 2100 block

Over the next two weeks expect to see:

Fire line to Copper Cellar tied to new main

Install water line L (next to Noodles)

Install insert-a-valve on existing water mains in Cumberland at 16th, in 17th, in North 18th and in North 19th.

> NOTE: Insert-a-valves are shutoff values added to water lines that allow for future work to be performed with minimal or no disruption of services.

Traffic shift between 17th and 16th to install final runs of water and gas to the end of project

Install storm drainage in 17th

Continue electrical service conversions in 17th Street

Continue pervious pavers in the 2100 and 2000 blocks

> NOTE: Pervious pavers allow stormwater to percolate through the surface rather than running off into surrounding areas or storm drains. As water runs through, the pavers filter urban pollutants. Like grass, pervious pavers let the ground below breathe. These pavers also allow tree roots

and their supporting microbes to interact. (Source: Water Environment Federation, 2013).

- Continue pouring sidewalks and planters in the 1900 block
- Continue silva cell installation in the 1800 block

Two-Week Look Ahead

May 26, 2016

PLEASE BE AWARE AND SHARE...

During the past week

- Water services installed across 17th
- Sewer work in south alley will be completed end of week (May 27)
- Storm drainage in Cumberland instlled to 17th
- Electrical duct bank installed across 17th
- Tree well and Silva cell excavation has progressed to Half Barrel
- Sidewalks poured to Studio X
- Paver installation has begun in 2100 block (Cookout to Mellow Mushroom)
- North alley between 18th and 19th has been repaved (Copper Cellar to Regions)
- Repaving of business entrances from 22nd to University Liquors

Over the next two weeks expect to see:

- Complete installation of water line K (next to Walgreens) in North 18th
- Install water line L (next to Noodles)
- Install insert-a-valve on existing water mains in Cumberland at 16th, in 17th, in North 18th and in North 19th.

  NOTE: Insert-a-valves are shutoff values added to water lines that allow for future work to be performed with minimal or no disruption of services.
- Install storm drainage in 17th Street
- Continue electrical service conversions in 17th Street
- Pervious pavers in the 2100 and 2000 blocks

  NOTE: Pervious pavers allow stormwater to percolate through the surface rather than running off into surrounding areas or storm drains. As water runs through, the pavers filter urban pollutants. Like grass, pervious pavers let the ground below breathe. These pavers also allow tree roots and their supporting microbes to interact. (Source: Water Environment Federation, 2013).
- Complete curbs and sidewalks in the 2000 block
- Continue pouring sidewalks and planters in the 1900 block
- Continue silva cell installation in the 1800 block

Two-Week Look Ahead

May 19, 2016

PLEASE BE AWARE AND SHARE...

The following closures will be occuring this week:

- Full closure of parking spaces in Melrose Place on Tuesday and Wednesday
-

Overnight closure (10pm - 6am) of Cumberland between 18th and 17th, Monday thru Wednesday

- Full closure of south alley between 18th and 19th
- Closure of southbound lane of 17th Street
- Overnight closures (10pm - 6am) of 17th street Monday thru Wednesday

During the past week

- Sewer line installed in South 18th, and repaved
- Water and gas services are complete to 17th except for Copper Cellar
- Gas main connection in Melrose is complete
- Storm drainage in Cumberland installed to Smoke Rings
- Electrical duct banks in 17th installed from north alley to Fort Sanders Yacht Club
- Tree well and Silva cell excavation has progressed to Regions Bank
- Sidewalks poured up to radius at 20th
- Entrance to University Liquors poured
- Roadway curbs poured to Piano Bar at North 19th

Over the next two weeks expect to see:

- Install sewer in the south alley between 18th and 19th street
- Install water services in 17th
- Complete installation of water line K in North 18th
- Install insert-a-valve on existing waterline in Cumberland at 16th
- Install insert-a-valve on existing waterling in North 19th
- Continue north side storm drainage installation in mainlin Cumberland to 17th
- Complete installation of street lighting, special events duct banks, and electrical service conversions in 17th Street
- Installation of pervious pavers in the 2100 block
- Complete curbs and sidewalks in the 2000 block
- Continue pouring sidewalks and planters in the 1900 block
- Continue silva cell installation in the 1800 block

Two-Week Look Ahead

May 12, 2016

PLEASE BE AWARE AND SHARE...

There will be an overnight full closure (10pm - 6am) of Cumberland Avenue between 19th Street and 17th Street beginning Monday, May 16 through Wednesday, May 18 for the installation of new water services across Cumberland. Traffic will be detoured around the area.

During the past week

- Water line J (near McDonald's and Moe's) installed in South 18th
- Water and gas services to properties are being connected to the new mains
- Storm Drainage in Cumberland installed to Walgreens
- Electrical duct banks installed to North 18th
- Tree well and Silva cell excavation has progressed to North 19th
- Sidewalks poured up to radius North 20th
- Roadway curb poured to University Liquors

Over the next two weeks expect to see:

- Complete connecting service lines to new main from 19th to 18th
- Install insert-a-valve on existing waterline in Cumberland at 16th

Install sewer in South 18th and the south alley between 18th and 19th

- Complete connecting service lines to new mains from 19th and 18th
- Complete installation of water line K (near Walgreen's) in North 18th
- Continue installing service lines in Cumberland from 18th to 17th
- Install insert-a-valve on existing waterline in Cumberland at 16th
- Install insert-a-value on exitisting waterline in North 19th
- Continue north side storm drainage installation in mainline Cumberland to 17th
- Begin street lighting, special events duct banks, and electrical service conversions in 17th Street
- Begin installation of pervious pavers in the 2100 block
- Complete curbs and sidewalks in the 2000 block
- Continue pouring curbs and sidewalks in the 1900 block

Two-Week Look Ahead

May 5, 2016

PLEASE BE AWARE AND SHARE...

Knoxville Utilities Board electrical system upgrades to support construction of a large apartment complex in Fort Sanders will require overnight street closures, starting tonight (Tuesday, May 3) and continuing through Friday morning, May 13. The Standard is a 240-plus-unit apartment complex being built on the southwest corner of 17th Street and White Avenue.

For the next week and a half, motorists should anticipate the closure of North 18th Street between Cumberland and White avenues nightly, from 6 p.m. until 6 a.m. the following morning.

Similarly, two lanes will be closed nightly on 17th Street, between Cumberland and Clinch avenues, from 6 p.m. until 6 a.m. the following morning. The alley between 18th and 17th (north of Cumberland and south of White) will not be accessible during the overnight construction.

During the past week

- Gas risers installed in 17th
- Water main in Cumberland has been tested and is in service to 18th
- Water and gas servies to properties are being connected to the new mains
- Storm Drainage in Cumberland installed to 18th
- Electrical duct banks installed to Copper Cellar entrance
- Tree well and Silva cell excavation has progressed to North 19th
- Sidewalks will poured to the radius at North 20th by end of day Friday, May 6
- Roadway curb construction has progressed to North 20th at Stefano's

Over the next two weeks expect to see:

- Complete connecting service lines to new main from 19th to 18th
- Install insert-a-valve on existing waterline in Cumberland at 16th
- Complete installation of water line K (near Walgreen's) in North 18th
- Continue installing service lines in Cumberland from 18th to 17th
- Continue north side storm drainage installation in mainline Cumberland to 17th
- Continue street lighting and special events duct banks on the North side of Cumberland to 18th then advance to 17th for electrical service conversions
- Continue constructing the furnishing zone in the 2000 block
-

Complete curbs and sidewalks in the 2000 block

Begin pouring curbs and sidewalks in the 1900 block

Two-Week Look Ahead

April 28, 2016

PLEASE BE AWARE AND SHARE...

If you are visiting merchants on the North side of the street (i.e. Starbucks, Mellow Mushroom, University Liquors, Copper Cellar, Walgreens, FedEx Office, etc.) you will need to come in from 17th Street or Westbound Cumberland from downtown. For merchants on the South side (i.e. Sunspot, Panera Bread, Jason's Deli, Oscar's Italian, Moe's, McDonalds, Krystal, Hilton Garden Inn, etc.) access is from Volunteer Blvd., University Commons, Alcoa Highway or East Bound on Kingston Pike.

During the past week

- Long (South) side water services installed to McDonald's
- Water main in Cumberland is filled to 18th and is currently being tested
- Storm Drainage in Cumberland delayed by fire line conflict at Copper Cellar
- Electrical duct banks installed to mid-block between 19th and 18th
- Tree well and Silva cell excavation has progressed to mid-block between 20th and 19th
- All concrete has been poured between North 22nd and North 21st except for corner at Cumberland and 22nd
- Sidewalks have been poured to mid-block between North 21st and North 20th
- Roadway curb consturction has progressed to North 21st

Over the next two weeks expect to see:

- Connect services to new gas main and condemn existing line through 17th
- Complete testing of water main from South 19th Street to 18th Street
- Begin connecting service lines to new main from 19th to 17th
- Install insert-a-valve on existing waterline in Cumberland at 16th
- Begin installation of water line J (Next to McDonald's) in South 18th
- Continue installing service lines in Cumberland from 18th to 17th
- Continue north side storm drainage installation in mainline Cumberland to 18th then advance to 17th for electrical service conversions
- Continue construction the furnishing zone in the 2100 and 2000 blocks
- Complete curbs and sidewalks in the 2000 block
- Begin pouring curbs and sidewalks in the 1900 block

Two-Week Look Ahead

April 21, 2016

PLEASE BE AWARE AND SHARE...

If you are visiting merchants on the North side of the street (i.e. Starbucks, Mellow Mushroom, University Liquors, Copper Cellar, Walgreens, FedEx Office, etc.) you will need to come in from 17th Street or Westbound Cumberland from downtown. For merchants on the South side (i.e. Sunspot, Panera Bread, Jason's Deli, Oscar's Italian, Moe's, McDonalds, Krystal, Hilton Garden Inn, etc.) access is from Volunteer Blvd., University Commons, Alcoa Highway or East Bound on Kingston Pike.

During the past week

- Gas main has been tested and is active up to 17th
- Long (South) Side water services are installed to Moe's
- Installation of water line H in North 19th (near Regions Bank) is complete

- Storm drainage in Cumberland is up to Copper Cellar
- Special events duct banks installed across Cumberland at 20th and 19th
- Tree well and Silva cell excavation has progressed to mid-block between 20th and 19th
- Entrance to Starbucks and western entrance to Shell are poured
- Roadway curb construction has progressed to Shell

Over the next two weeks expect to see:

- Connect services to new gas main and condemn existing line through 17th
- Fill and begin testing of water main from South 19th Street to 18th Street
- Complete installation of water line K (next to Walgreens) in North 18th
- Begin installation of water line J (Next to McDonald's) in South 18th
- Continue installing service lines in Cumberland from 18th to 17th
- Resume north side storm drainage installation in mainline Cumberland
- Continue street lighting and special events duct banks on the North side of Cumberland
- Complete curbs and sidewalks in the 2100 block
- Continue construction the furnishing zone in the 2100 block
- Continue pouring curbs and sidewalks in the 2100 block

Two-Week Look Ahead

April 14, 2016

PLEASE BE AWARE AND SHARE...

There will be overnight closures of Cumberland on Monday, April 18, Tuesday, April 19 and Wednesday, April 20th to install south side water serivces to merchants.

If you are visiting merchants on the North side of the street (i.e. Starbucks, Mellow Mushroom, University Liquors, Copper Cellar, Walgreens, FedEx Office, etc.) you will need to come in from 17th Street or Westbound Cumberland from downtown. For merchants on the South side (i.e. Sunspot, Panera Bread, Jason's Deli, Oscar's Italian, Moe's, McDonalds, Krystal, Hilton Garden Inn, etc.)access is from Volunteer Blvd., University Commons, Alcoa Highway or East Bound on Kingston Pike.

During the past week

- Water line H in North 19th is installed almost to White Avenue
- Water main connection in Sumberland at South 19th is complete
- South side water services are installed to Goal Post Tavern
- Storm drainage in Cumberland has progresses to Copper Cellar
- Overhead electrical removals from North 20th to North 18th are complete
- Street lighting duct bank installation in North 19th continues
- Tree well and Silva cell installation has progressed to mid-block between 20th and 19th
- Entrances in 2100 block are all poured and re-opened
- Roadway curb construction has progressed to Starbucks

Over the next two weeks expect to see:

- Complete installation of water line H in North 19th
- Complete installation of water line K in North 18th
-

Install water line J in South 18th week of April 25

- Continue installing service lines in Cumberland from 19th to 17th Streets
- Continue north side storm drainage installation in mainline Cumberland
- Continue street lighting and special events duct banks on the North side of Cumberland
- Continue pouring curbs and sidewalks in the 2100 block
- Continue constructing the furnishing zone in the 2100 block
- Begin curbs and sidewalks in the block between North 21st and North 20th

Two-Week Look Ahead

April 7, 2016

PLEASE BE AWARE AND SHARE...

There will be an overnight closure of 17th on Thursday, April 7, 2016 between Cumberland and White to for utility work. Additional overnight closures of Cumberland between 19th Street and 17th Streets will occur on Monday, April 11, Tuesday, April 12, and Wednesday, April 13 to install south side water serivces to merchants.

If you are visiting merchants on the North side of the street (i.e. Starbucks, Mellow Mushroom, University Liquors, Copper Cellar, Walgreens, FedEx Office, etc.) you will need to come in from 17th Street or Westbound Cumberland from downtown. For merchants on the South side (i.e. Sunspot, Panera Bread, Jason's Deli, Oscar's Italian, Moe's, McDonalds, Krystal, Hilton Garden Inn, etc.)access is from Volunteer Blvd., University Commons, Alcoa Highway or East Bound on Kingston Pike.

During the past week

- Water line H in North 19th is being installed
- North side water services are installed to 17th
- Storm drainage in Cumberland has been installed to Regions Bank
- Street lighting duct bank installation has progressed to North 19th
- Tree well and Silva cell installation has progressed to Stefano's
- North side sidewalks have been poured to Mellow Mushroom
- First pour of colored concrete begins Thursday, April 7
- Roadway curb in the first block completed by Friday, April 8

Over the next two weeks expect to see:

- Complete installation of water line H in North 19th
- Complete installation of water line K in North 18th
- Install water line J in South 18th
- Compete main connection in South 19th
- Continue installing service lines in Cumberland from 19th to 17th Streets
- Resume overhead electrical removals from North 20th to North 18th
- Resume north side storm drainage installation in mainline Cumberland at N. 19th headed east
- Continue street lighting and special events duct banks on the North side of Cumberland
- Continue pouring curbs and sidewalks in the block between North 22nd and North 21st
- Continue constructing the furnishing zone in the block between North 22nd and North 21st
- Begin curbs and sidewalks in the block between North 21st and North 20th

Two-Week Look Ahead

March 31, 2016

PLEASE BE AWARE AND SHARE...

The Standard apartment complex will have 17th Street reduced to one lane in each direction, the alley between 17th and 18th Streets closed and the intersection of the alley in 18th Street closed on

Friday, April 1 from 7am until 5pm in order to video the sewer line. An additional closure will be needed to finish sewer work within the next couple of weeks.

If you are visiting merchants on the North side of the street (i.e. Starbucks, Mellow Mushroom, University Liquors, Copper Cellar, Walgreens, FedEx Office, etc.) you will need to come in from 17th Street or Westbound Cumberland from downtown. For merchants on the South side (i.e. Sunspot, Panera Bread, Jason's Deli, Oscar's Italian, Moe's, McDonalds, Krystal, Hilton Garden Inn, etc.)access is from Volunteer Blvd., University Commons, Alcoa Highway or East Bound on Kingston Pike.

During the past week water and gas main are installed to 17th Street intersection, water line K in North 18th has been installed to the alley, short side water services are installed to mid-block between North 19th and North 18th, storm manhole 14A installed at Mellow Mushroom, street lighting duct bank installation has progressed to mid-block between North 20th and North 19th, tree well and silva cell installation has progress to North 20th and north side sidewalks have been poured to Insomnia Cookies.

Over the next two weeks expect to see:

- Complete installation of water line H in North 19th
- Resume installation f water line K in North 18th
- Complete main connection in South 19th, overnight closure of Cumberland will be required
- Continue installing service lines in Cumberland from 19th to 17th
- Shift traffic at 17th intersection to allow installation of water and gas mains in the east bound lanes of Cumberland Avenue east of 17th
- Resume overhead electrical removals from North 20th to North 18th
- Resume north side storm drainage installation in mainline Cumberland at N. 19th headed east
- Continue street lighting and special events duct banks on the North side of Cumberland
- Continue pouring curbs and sidewalks in the block between North 22nd and North 21st
- Begin constructing the furnishing zone in the block between North 22nd and North 21st

Two-Week Look Ahead

March 24, 2016

PLEASE BE AWARE AND SHARE...

If you are visiting merchants on the North side of the street (i.e. Starbucks, Mellow Mushroom, University Liquors, Copper Cellar, Walgreens, FedEx Office, etc.) you will need to come in from 17th Street or Westbound Cumberland from downtown. For merchants on the South side (i.e. Sunspot, Panera Bread, Jason's Deli, Oscar's Italian, Moe's, McDonalds, Krystal, Hilton Garden Inn, etc.)access is from Volunteer Blvd., University Commons, Alcoa Highway or East Bound on Kingston Pike.

During the past week the gas line across Cumberland at South 21st has been installed, water line M installation in 17th Street is complete, water and gas main are installed up to mid-block between 18th and 17th, cable has been pulled through the primary duct bank in 18th, electrical service conversion to Steffano's is complete, street lighting duct bank installation complete to University Liquors, storm drainage installation in North 20th is complete, tree well and silva cell installation has progressed to the Shell station and the roadway curb has been pured to Insomnia Cookies.

Over the next two weeks expect to see:

- Begin installation of water line K in North 18th
- Begin installation of water line H in North 19th
- Complete service connections in South 19th
- Begin installing service lines in Cumberland from 19th to 17th
- Resume overhead electrical removals from North 20th to North 18th
- Install the added storm manhole 14A at Mellow Mushroom
- Complete storm drainage in North 19th
- Resume north side storm drainage installation in mainline CUmberland at N. 19th headed east
-

Continue street lighting and special events duct banks on the North side of Cumberland

- Continue pouring curbs and sidewalks in the block between North 22nd and North 21st

Two-Week Look Ahead

March 17, 2016

Delineators have now been placed up to 17th, which prohibits left hand turns. Remember...if you are visiting merchants on the North side of the street (i.e. Starbucks, Mellow Mushroom, University Liquors, Copper Cellar, Walgreens, FedEx Office, etc.) you will need to come in from 17th Street or Westbound Cumberland from downtown. For merchants on the South side (i.e. Sunspot, Panera Bread, Jason's Deli, Oscar's Italian, Moe's McDonalds, Krystal, Hilton Garden Inn, etc.) you will need to come in from Alcoa Highway or East Bound on Kingston Pike.

During the past week water and gas mains were installed through the 17th Street intersection, water line installation in 17th street is ongoing, connections of services to the new water systerm are complete to North 19th, storm drainage installation in North 19th is complete to structure 62, electrical service conversion to Region's Bank is complete, tree well and silva cell installation has progressed to Starbucks.

Over the next two weeks expect to see:

- Begin installation of water line K in North 18th
- Begin installation of water line H in North 19th
- Continue to tie over water mains and services in South 19th to existing water system
- Continue installation of water and gas in mainline Cumberland
- Electrical service conversion to Steffano's scheduled for week of March 21
- Resume overhead electrical removals from North 20th to North 18th
- Pull high voltage cable through new duct bank in North 18th
- Complete storm drainage in North 20th by week of March 30
- Complete storm drainage in North 19th by week of March 30
- Continue street lighting and special events duct banks on the North side of Cumberland
- Begin pouring concrete in the block between North 22nd and North 21st

Two-Week Look Ahead

March 10, 2016

Delineators have now been placed up to 17th, which prohibits left hand turns. Remember...if you are visiting merchants on the North side of the street (i.e. Starbucks, Mellow Mushroom, University Liquors, Copper Cellar, Walgreens, FedEx Office, etc.) you will need to come in from 17th Street or Westbound Cumberland from downtown. For merchants on the South side (i.e. Sunspot, Panera Bread, Jason's Deli, Oscar's Italian, Moe's McDonalds, Krystal, Hilton Garden Inn, etc.) you will need to come in from Alcoa Highway or East Bound on Kingston Pike.

During the past week Tie-ins and connections of new services to new water system are ongoing, a. Storm drainage installation in North 19th is ongoing, storm in alley between 13th and 19th is complete to structure 63 behind Niro's Gyros, electrical service conversion to Region's Bank schedule to be completed by Saturday, 3/12 and tree well and silva cell installation has progressed to Mellow Mushroom.

Over the next two weeks expect to see:

- Install water line M in 17th
- Continue to tie over water services from 21st to North 19th to new water system
- Resume installation of water and gas in mainline Cumberland at North 19th heading east
- Complete storm drainage in North 20th
- Complete storm drainage in North 19th
- Continue street lighting and special events duct banks on the North side of Cumberland
- Continue rebuilding the block between North 22nd and North 21st

Two-Week Look Ahead

March 3, 2016

Delineators have now been placed up to 17th, which prohibits left hand turns. Remember...if you are visiting merchants on the North side of the street (i.e. Starbucks, Mellow Mushroom, University Liquors, Copper Cellar, Walgreens, FedEx Office, etc.) you will need to come in from 17th Street or Westbound Cumberland from downtown. For merchants on the South side (i.e. Sunspot, Panera Bread, Jason's Deli, Oscar's Italian, Moe's McDonalds, Krystal, Hilton Garden Inn, etc.) you will need to come in from Alcoa Highway or East Bound on Kingston Pike.

During the past week Fire service to Evolve has been tied in, sewer testing continues on need lines, tie-ins and connections of new services to the new water system are ongoing, North side storm drainage has been installed to structure 20A, storm sewer in alley between 18th and 19th will be installed by 3/12/16, North side overhead electrical has been removed to North 20th, electrical duct bank installed to Shell station, and first tree wells and silva cells are being installed in front of Cook Out.

Over the next two weeks expect to see:

- The Closure of Cumberland at 17th street March 12-14 (5 AM to 6 AM)
- Complete storm drainage in North 20th
- Continue Phase 2 storm drainage on the north side of Cumberland and in North 19th
- Continue street lighting and special events duct banks on the North side of Cumberland
- Begin rebuilding the block between North 22nd and North 21st.

Two-Week Look Ahead

February 25, 2016

As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward to 17th Street.

During the past week Pipe burst sewer installation in alley behind Copper Cellar is complete, MAJOR MILESTONE ACHIEVED: All sewer on the Streetscapes project has been installed, tie-ins and connections of new services to new water system are ongoing, North side storm drainage installed to structure 19 (just past University Liquors), storm drainage in North 20th installed to structure 56, and the special events duct bank has been installed to Starbucks.

Over the next two weeks expect to see:

- Complete storm drainage in North 20th
- Continue Phase 2 storm drainage on the north side of Cumberland and in North 19th
- Removal of the north side overhead electrial and utility poles from Volunteer to North 20th to begin Thursday 2/25.
- Continue street lighting and special events duct banks on the North side of Cumberland
- Begin rebuilding the block between North 22nd and North 21st starting with the silva cell excavation and building up.

Two-Week Look Ahead

February 18, 2016

As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward to 17th Street.

During the past week the testing of the new water system up to North 19th is complete (tie-ins and connections to new servies are ongoing); North 18th is now open to traffic; new valve installed on existing water line in front of Hannah's Cafe; North side storm drainage has been installed just past University Liquors and street lighting duct bank has been installed to Starbucks.

Over the next two weeks expect to see:

- Continue to tie over water services from 21st to North 19th to new water systerm
- Begin the installation of a new water line in North 19th
- Resume installation of water and gas in the mainline Cumberland at North 19th heading east
- Continue Phase 2 storm drainage on the north side of Cumberland and in North 20th
- Removal of the north side overhead electrial and utility poles from Volunteer to North 20th to begin Thursday 2/25 or Monday, 2/29.

Two-Week Look Ahead

February 11, 2016

As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward to 17th Street.

During the past week the new water system from 21st to 19th has been filled and sampled and pressure testing starts 2/11/2016; new sewer in the alley between North 19th and North 18th has been installed from manhole 33C to the existing manhole in North 18th; Pavement patching of 18th from the south alley to the north alley where the KUB primary electrical duct bank was installed is now complete; North side storm drainage has been installed to structure 18A in front of University Liquors; south side temporary lighting installation is complete; and overhead high voltage work at South 18th is complete and ready for KUB to make final connections.

Over the next two weeks expect to see:

- Continue Phase 2 storm drainage on the north side of Cumberland and in North 20th
- Install 30" storm drainage piping in the alley between 18th and 19th
- Removal of the north side overhead electrial and utility poles from Volunteer to North 20th

Two-Week Look Ahead

February 4, 2016

As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward to 17th Street.

During the past week gas services between North 20th and North 19th are geing tied over to the new main, all long side water service laterals and fire lines have been installed across Cumberland up to North 19th, sewer manholes 33B and 33C have been installed in the alley betweeen North 19th and North 18th, KUB primary electrial duct bank in North 18th is complete (pavement patching from the southa lley to the north alley will be completed by end of day 2/4/16), and the south side temporary lighting installation is underway and will be completed week of 2/8/2016.

Over the next two weeks expect to see:

- Complete sewer construction in alley between North 19th and North 18th (behind Copper Cellar) - one week left in duration due to weather delays
- Begin testing of new water system to North 19th
- Begin install of water line "H" in North 19th
- Continue Phase 2 storm drainage on the north side of Cumberland and in North 20th
- Install 30" storm drainage piping in the alley between 18th and 19th
- Complete south side temporary lighting (projected completion by Wednesday, 2/10/2016)

Two-Week Look Ahead

January 28, 2016

As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward to 17th Street.

During the past week the new 8" gas line has been tested and in service up to North 19th Street. Irrigation service and 6" line to Long Branch Saloon has been installed, Sewer in the alley between North 19th and North 18th has been installed at the NW corner of Copper Cellar's property, KUB primary electrical duct bank in North 18th has progressed and the north side storm drainage has been installed to the corner of North 20th.

Over the next two weeks expect to see:

- Continue sewer construction in alley between North 19th and North 18th (behind Copper Cellar), two weeks left due to weather.
- Install long side irrigation at South 19th
- Continue installation of primary electrical duct bank in North 18th
- Asphalt patching of 18th where KUB duct bank was installed

Continue Phase 2 storm drainage on the north side of Cumberland and in North 20th

- Install 30" storm drainage piping in the alley between 18th and 19th
- Continue south side temporary lighting

Two-Week Look Ahead

January 21, 2016

As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward to 17th Street.

During the past week the 4" fire service line to Panera has been installed, the sewer in the alley between North 19th and North 13th has been installed to manhole 33A at the corner NW corner of Copper Cellar's property, KUB Primary electrical duct bank in North 18th has begun - Rock excavation and weather has slowed progress this week - and North side storm drainage has been installed to structure in front of Shell station

Over the next two weeks expect to see:

- Continue sewer construction in alley between North 19th and North 18th (behind Copper Cellar), two weeks left in duration. Weather delays could extend that duration.
- Install long side irrigation service at Taco Bell as well as water line G across Cumberland at South 19th
- Continue installation of primary electrical duct bank in North 13th
- Continue Phase 2 storm drainage on the north side of Cumberland Ave.
- Install 30" storm drainage piping in the alley between 13th and 19th
- Begin installation of south side temporary lighting the week of 1/25/16, work scheduled for this week was delayed by weather

Two-Week Look Ahead

January 14, 2016

Over the past week, the installation of a water line was completed in North 20th. The sewer line in the alley between North 19th and North 18th (behind Copper Cellar) has progressed from 19th to the NW corner of Copper Cellar's property. The primary duct bank installation has been completed in South 18th, north side storm drainage installed to structure between Starbucks and Shell, storm drainage in North 21st is complete new signal arms have been installed on 17th and Clinch.

As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward to 17th Street.

Over the next two weeks expect to see:

- The Closure of Cumberland at 17th street March 12-14 (5 AM to 6 AM)
- Sewer construction continues in alley between North 19th and North 18th (behind Copper Cellar) - three week duration
- Continuation of Phase 2 Storm Drainage installation moving eastward toward 17th Street
- Continuation of the installation of primary electrical duct bank in South 18th in order to give KUB the ability to facilitate north side overhead electrical removals for Phase 2.
- Temporary street lighting on the south side between 22nd and 21st begins January 18, 2016.

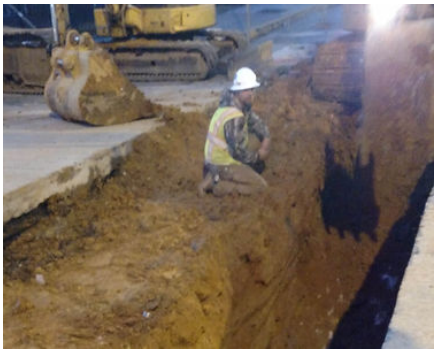

Two-Week Look Ahead

January 7, 2016

Over the past week, a sewer bypass is now in place for sewer replacement and rehab in the alley between North 19th and North 18th (behind Copper Cellar), water and gas has been in stalled through the 19th Street intersection, new water services have been installed to Panera Bread and Uptown Grill, the KUB primary electrical duct bank across Cumberland is complete (except for pavement patching), storm sewer drainage installed at North 21st Street and the KUB primary electrical duct bank is across 18th street.

As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward at the 19th Street and 18th Street locations.

Over the next two weeks expect to see:

- Sewer construction continues in alley between North 19th and North 18th (behind Copper Cellar) - four week duration
- A water line installation in South 19th Street
- Continuation of Phase 2 Storm Drainage installation moving eastward toward 17th Street
- Continuation of the installation of primary electrical duct bank in South 18th in order to give KUB the ability to facilitate north side overhead electrical removals for Phase 2.
- The beginning of the installation of south side temporary lighting (1/18/16).

Two-Week Look Ahead

December 31, 2015

Over the past week, we have installed the KUB primary electrical duct bank across Cumberland, installed North side storm drainage to underground structure 15, and installed a new water line and new sewer line in North 20th Street.

As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward toward 19th and 18th Streets.

Over the next two weeks expect to see:

- Sewer constrution in alley between North 19th and North 18th (behind Copper Cellar) - five week duration
- A new water line in South 19th Street
- Continuation of water and gas installation through 19th Street intersection
- Continuation of Phase 2 Storm Drainage installation moving eastward toward 17th Street
- Beginning of installation of south side temporary lighting

Two Week Look Ahead

December 21, 2015

Over the past two weeks, we have been able to put down the permanent pavement markings giving a finished look to the section of Cumberland Avenue between 22nd Street and Alcoa Highway. As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward toward 19th and 18th Streets.

Over the next two weeks expect to see:

- A complete closure of Cumberland between North 19th Street and 17th Street beginning 6am, Monday, 12/28/15 through 5pm, Tuesday, 1/5/16. This closure is to install a new KUB primary electrical duct bank. Click here to access traffic detour.
- New water line installation in North 20th and South 19th Streets
- The continuation of water and gass from 20th to 19th Streets
- The coninuation of storm sewer drainage installation heading east
- The addition of new sidewalks on the east side of South 22nd Street
- Installation of primary electrical duct bank in North 18th, which gives KUB the ability to facilitate north side overhead electrical removals
- Beginning of Phase II construction.

Two Week Look Ahead

December 3, 2015

This past week, we have been inundated with rain; however, work is still on schedule for both utility and streetscape construction. As you travel on Cumberland, please be patient with traffic delays as our construction crews work to keep our project moving forward.

Over the next two weeks expect to see:

- From 9am - 6pm each day through Friday 12/12 there will be Temporary lane closures and traffic pattern shifts to install stamped asphalt crosswalks. Flagmen and/or barrels will be used to maintain traffic.
- The new gas line tie-in at 22nd and the abandon of the old line from 22nd to 20th
- The continuation of the gas line installation from 20th and 19th Streets
- Installation of the new sewer line in North 19th Street to the North Alley

- Asphalt patching on 22nd Street
- 42" Storm Drainage installation continues eastward
- Work begins to transition into Phase II as Phase I comes to a close. Click here to see Phase II information.

Two Week Look Ahead

November 19, 2015

Work is still on schedule for both utility and streetscape construction. As you travel on Cumberland, you will see the centerline delineators and construction barricades continue to move eastward.

Over the next two weeks expect to see:

- The continuation of the gas line installation from 20th and 19th Streets
- Installation of a new sewer line in Cumberland between South 19th and North 19th Street
- 42" Storm Drainage installation will continue to move toward the east
- Permanent signs to be installed
- Completion of the new pavement from Voluteer to Alcoa Highway

UTILITY WORK TO CLOSE SECTION OF CUMBERLAND AVENUE

November 16, 2015

Starting at 6 a.m. Saturday, Nov. 21, and continuing until 6 a.m. Monday, Nov. 23, Cumberland Avenue will be closed between North 19th Street and 20th Street as crews install sewer system infrastructure.

Westbound motorists for those two days will be detoured using 19th Street to Clinch Avenue to 22nd Street. Eastbound motorists will follow the same detour route in reverse order.

Also, KUB's contractor, Southern Constructors, will implement a second road closure as part of the sewer system upgrades. Today through 6 a.m. Monday, Nov. 23, South 19th Street will be closed between Cumberland Avenue and Lake Avenue.

These two road closures are part of Phase II of the City of Knoxville's overall $17 million Cumberland Avenue reconstruction. Phase II, to be completed in August 2017, will change the existing four-lane street to a three-lane cross section with a raised median and left-turn lanes at intersections between 22nd Street and 17th Street.

Meanwhile, Phase I work – improving traffic flow between the Alcoa Highway ramps and 22nd Street – is coming to a close ahead of schedule. Last Friday, Nov. 13, barrels were removed and all five lanes of traffic reopened.

On Thursday, Nov. 19, the last lane in the Phase I area is being repaved, so anticipate some lane shifts on that day.

In both the Phase I and Phase II projects, Cumberland Avenue sidewalks are being widened and landscaped, and utility lines relocated, to create a more attractive, safer, pedestrian-friendly corridor. Utility infrastructure is being updated.

Unrelated to the City's Cumberland Avenue project: From 1 p.m. Friday, Nov. 20, through 9 p.m. Sunday, Nov. 22, White Avenue will be closed between 20th and 21st streets. A crane used in the construction of a new East Tennessee Children's Hospital building is being dismantled

Two Week Look Ahead

November 5, 2015

Work is still on schedule for both utility and streetscape construction. As you travel on Cumberland, you will continue to see the centerline delineators and construction barricades move eastward.

Over the next two weeks:

- New water connections at 21st & Lake and 21st & White will be completed
- Construction of sewer line in North 21st Street will be completed
- New sewer line installation begins in South 19th Street
- The 42" storm sewer continues to move toward 20th Street
- The final laydown of new pavement will begin from from Alcoa Highway to 22nd
- The new signal systems will be completed at University Commons and Volunteer Blvd.

Two Week Look Ahead

October 29, 2015

Both utility and streetscape construction are still on schedule, even though we have had some weather issues to contend with.

Over the next two weeks expect to see:

- The completion of the new sidewalks on the west side of North 22nd Street
- Completion of underground electric on north side of Cumberland across 22nd
- The continuation of the 42" storm drainage moving east near 20th Street
- Installation of silva cells near Cookout - silva cells provide underground root space for the new tree plantings.

We will continue to provide weekly updates as we move forward with the streetscape transformation.

Two Week Look Ahead

October 22, 2015

Construction continues to track on schedule for the Cumberland Avenue streetscape transformation.

Over the next two weeks expect to see:

- the undergrounding of electric utilities on the North Side of Cumberland across 22nd Street
- New sidewalks on the west side of North 22nd Street
- Additional Storm Drainage being constructed on the North side of Cumberland - moving east near 20th Street
- New silva cell installation in front of Cookout - Silva cells provide underground root space for the news trees to be planted as part of the streetscape transformation.

More updates to come over the next few weeks as we being to close Phase I and enter into Phase II.

WATER LINE INSTALLATIONS PROMPT NIGHT-TIME CLOSURE OF 2 BLOCKS OF CUMBERLAND AVENUE, STARTING TONIGHT

September 28, 2015

A contractor will be installing and connecting water lines on Cumberland Avenue this week, prompting the overnight closure of Cumberland for four nights, starting tonight.

Cumberland Avenue between 20th and 22nd streets will be closed at 10 p.m. tonight and will reopen at 6 a.m. Tuesday. The closures will be repeated Tuesday, Wednesday and Thursday nights, with the road reopening at 6 a.m. the following morning.

Westbound motorists on Cumberland Avenue will be detoured right onto 20th Street, left onto Clinch Avenue and left onto 22nd Street to reconnect to westbound Cumberland.

Eastbound motorists will be detoured right onto 22nd Street, left onto Terrace Avenue and left onto 19th Street to reconnect to eastbound Cumberland.

Southern Contractors Inc. will be completing the installations – connecting customers to new infrastructure, with no planned service interruptions – as part of an upgrade of utilities in the Cumberland Avenue Corridor by KUB, in partnership with the City of Knoxville.

LANE CLOSURES SCHEDULED IN CUMBERLAND AVENUE CORRIDOR

September 15, 2015

Work associated with both the Cumberland Avenue reconstruction and the building of The Standard apartment complex will prompt several road closures in the Cumberland Avenue Corridor, starting today.

- From 9 a.m. to 3 p.m. today through Friday, Sept. 18, anticipate intermittent short-term partial closures on a section of 17th Street near White Avenue and Clinch Avenue as underground utilities are mapped out in preparation of new traffic signals being installed.

- Then, from 7 a.m. to 5 p.m. Thursday, Sept. 17, a section of White Avenue between 17th and 18th streets will be closed due to work associated with construction of The Standard, a 240-plus-unit apartment complex being built on the southwest corner of 17th Street and White Avenue. (The daytime closure will limit after-hour noise.)

- All next week – from Monday, Sept. 21, through Sunday, Sept. 27 – a section of North 22nd Street will be closed between Cumberland Avenue and the driveways to Exxon and the Cook Out to accommodate installation of a 30-inch storm drain across North 22nd Street. During the closure, there will be no access to or from 22nd Street on the north side of Cumberland

Avenue, but traffic flow on Cumberland itself will not be affected. The Exxon and Cook Out will have entrances to their parking lots open from 22nd Street. The sidewalk will be open on the east side of N. 22nd Street. (The closure is scheduled for a full week this week to take advantage of the University of Tennessee playing football at the University of Florida, thus avoiding closing the street on days near a home game in Knoxville.)

The stormwater upgrade is part of the City of Knoxville's $17 million reconstruction of Cumberland, which will modernize aging infrastructure and change the existing four-lane street to a three-lane cross section with a raised median and left-turn lanes at intersections. Sidewalks will be widened and landscaped, and utility lines relocated, to create a more attractive, safer, pedestrian-friendly corridor.

21st STREET CLOSURE EXTENDED ONE DAY

August 18, 2015

Due to delays related to wet weather, the closure of 21st Street at the north side of its intersection with Cumberland Avenue has been extended by one day. Crews started Monday with installation of water and gas pipelines across 21st Street, and the street is now scheduled to reopen by 5 p.m. on Thursday, Aug. 20, weather permitting.

During the closure, there is no access to or from 21st Street on the north side of Cumberland Avenue, but traffic flow on Cumberland itself is not affected. Nearby businesses Mellow Mushroom and Starbucks will have entrances to their parking lots open on both Cumberland and 21st Street.

21st STREET TO BE CLOSED AT CUMBERLAND AVE. AUG. 17-19

August 14, 2015

Construction crews will close 21st Street at the north side of its intersection with Cumberland Avenue next week, to install water and gas pipelines across 21st Street. The closure is scheduled to begin at 7 a.m. on Monday, Aug. 17, and will be finished by 5 p.m. on Wednesday, Aug. 19.

During the closure, there will be no access to or from 21st Street on the north side of Cumberland Avenue, but traffic flow on Cumberland itself will not be affected. Surrounding businesses Mellow Mushroom and Starbucks will have entrances to their parking lots open on both Cumberland and 21st Street.

CUMBERLAND AVENUE IS NOW OPEN TO BOTH EASTBOUND AND WESTBOUND TRAFFIC!

August 1, 2015

This major milestone has been reached and just in time for The University of Tennessee student move-in day!

MAJOR MILESTONE' ON CUMBERLAND AVENUE RECONSTRUCTION: EASTBOUND LANE TO REOPEN SATURDAY, AUG. 1

July 31, 2015

An eastbound lane will open Saturday, Aug. 1, on Cumberland Avenue between Alcoa Highway and 22nd Street – marking a "major milestone" in the City of Knoxville's $17 million reconstruction of Cumberland.

The Phase I work – upgrading aging utilities, improving traffic flow and adding Streetscape amenities on the western section of Cumberland Avenue – remains on schedule for completion by the end of 2015.

"This represents a big step forward for all Cumberland Avenue stakeholders," said Anne Wallace, the City's project manager and incoming Deputy Director of the Office of Redevelopment.

"Reopening traffic in both directions, prior to the University of Tennessee starting fall classes and the beginning of UT football, is

a major milestone in Phase I. The project remains on schedule."

...MORE

Closure of 21st Street

July 30, 2015

Beginning at 7am Monday, 8/3/2015 until 5pm Friday, 8/7/2015, 21st Street will be closed on the north side of Cumberland Avenue to install new sewer main. Traffic on Cumberland will be maintained in each direction. During closure, both entrances to Mellow Mushroom and both entrances to Starbucks will remain open.

STORM DRAINAGE INSTALLATION AT SUNSPOT AND JASON'S DELI...

July 20, 2015

S. 22nd Street will be closed from Monday, 7/20 through 5pm Wednesday, 7/22 to facilitate installation of storm drainage.

Through-traffic from N. 22nd Street to Lake Avenue can detour left on Cumberland, right on S. 21st Street to Lake Avenue.

WATER LINE RELOCATION SUCCESSFULLY COMPLETED!

July 12, 2015

The 16" water tap went well over the weekend and the roadway was paved back Saturday night. Westbound Cumberland and University Commons are now back open to traffic.

WATER LINE RELOCATION TO CLOSE TWO-BLOCK SECTION OF CUMBERLAND AVENUE

July 9, 2015

From 3 a.m. Saturday, July 11, through 6 a.m. Monday, July 13, a westbound lane of Cumberland Avenue will be closed between Volunteer Boulevard and the ramps east of Alcoa Highway. The practical effect will be a complete closure of all lanes in this two-block section of Cumberland Avenue for 51 hours.

Crews will be rerouting a water line around a 42-inch stormwater line deep below Cumberland Avenue.

Two eastbound lanes and two westbound lanes of Cumberland Avenue already are closed between University Commons and West Volunteer Boulevard. The weekend water line relocation will temporarily close the single westbound lane that's currently open through that area.

The rerouting of the water line will close the University Commons Way intersection at Cumberland Avenue. Shoppers or diners wishing to access the University Commons retail complex may do so via Joe Johnson Drive and Neyland Drive.

The utility work also will close the intersection of Volunteer Boulevard at Cumberland Avenue and the entrance to Metron Center Way from Cumberland Avenue.

The City of Knoxville's $17 million initiative to redesign Cumberland Avenue from Alcoa Highway east to 17th Street is changing the existing four-lane street to a three-lane cross section with a raised median and left-turn lanes at intersections. Sidewalks will be widened and landscaped, and utility lines relocated, to create a more attractive, safer, pedestrian-friendly corridor.

Construction is proceeding in two phases, with Phase I (from Alcoa Highway to 22nd Street) to be completed by the end of 2015, and Phase II (from 22nd Street to just east of 17th Street) scheduled for completion in August 2017.

After this weekend's full closure of the two-block section, one westbound lane on Cumberland Avenue will reopen Monday morning, July 13. Then, by Aug. 1, one eastbound lane will reopen. There will be one lane of traffic in each direction – eastbound and westbound – through the end of the year as Phase I work is completed.

UNDERGROUND UTILITY WORK TO CLOSE LANES ON TWO-BLOCK SECTION OF 17th STREET

June 29, 20215

Starting at 7 a.m. Tuesday, June 30, two of the four lanes on 17th Street between Clinch Avenue and Cumberland Avenue will be closed.

The closures on the two-block section of 17th Street will allow utility work that is part of the construction of The Standard, a 240-plus-unit apartment complex being built on the southwest corner of 17th Street and White Avenue.

The work – underground electrical and communication duct bank construction – will continue into August. One northbound lane and one southbound lane on 17th Street will remain open through the two-block section. The sidewalk on the west side of 17th Street also will be closed.

The 17th Street closures are not directly part of the City of Knoxville's Cumberland Avenue redesign project. However, Bob Whetsel, the City's Director of Redevelopment, believes the City's investment in infrastructure in the Cumberland Avenue Corridor is helping to successfully leverage major private reinvestment in the area.

"The City is committing $17 million in local and federal funds into the Cumberland project," Whetsel said. "When the redesign is completed in 2017, traffic will flow better, utility lines will have been relocated, and sidewalks will be wider and landscaped. Cumberland visitors and residents will enjoy a more attractive, safer, pedestrian-friendly corridor.

"The public investment is helping to stimulate dramatic redevelopment – more than $130 million in private investments – along the Cumberland Avenue Corridor, including The Standard."

Week End Closure A Success!

June 29, 2015 4:59 pm

The westbound lane and access to University Commons from Cumberland are now open! Thank you for your patience as the new 42" storm water pipe was successfully installed!

TWO-BLOCK SECTION OF CUMBERLAND AVENUE TO COMPLETELY CLOSE FRIDAY THROUGH MIDDAY MONDAY

June 24, 2015

Starting Friday morning, all lanes of Cumberland Avenue, in both directions, will be closed between 22nd Street and the ramps east of Alcoa Highway. Crews will be continuing to install a new 42-inch stormwater line 12 feet below Cumberland Avenue and rebuilding the at-grade railroad crossing in that section of Cumberland.

The closure of the two-block section of Cumberland Avenue will start at 10 a.m. Friday, June 26, and will continue through noon Monday, June 29.

The work will close University Commons Way at Cumberland Avenue. Shoppers or diners wishing to access the University Commons retail complex may do so via Joe Johnson Drive and Neyland Drive. **MORE >>>**

TOWING TO BEGIN ON CUMBERLAND AVENUE SIDE STREETS

June 22, 2015

Crews last Monday began reworking the traffic flow on streets feeding into the eastern end of Cumberland Avenue. Cars parked illegally on these side streets will be towed, starting Tuesday, June 23.

Four streets are being converted from one-way to two-way traffic – 18th, 19th south of Cumberland, Mountcastle and 21st Street – between Lake and White avenues. (There is already two-way traffic on 20th Street and on 19th Street north of Cumberland.) The change in traffic flow will make it easier for motorists to get to a particular business by giving drivers new options to more quickly reach their destinations. **MORE >>>**

SECTION OF CUMBERLAND AVENUE, UNIVERSITY COMMONS WAY TO TEMPORARILY CLOSE

June 22, 2015

Two major street closures are scheduled next week as milestones are met and work progresses on the City of Knoxville's Cumberland Avenue Corridor Project:

- The entrance to the University Commons shopping center from Cumberland Avenue will be closed Monday, June 22, through Thursday, June 25, while construction crews connect stormwater quality devices with the Cumberland Avenue stormwater line. University Commons will remain accessible from Joe Johnson Drive, via Neyland Drive.
- From 10 a.m. Friday, June 26, through noon Monday, June 29, all lanes of Cumberland Avenue, in both directions, will be closed between 22nd Street and the ramps east of Alcoa Highway. Crews will be installing a stormwater line and rebuilding the railroad crossing in that section of Cumberland Avenue. **MORE >>>**

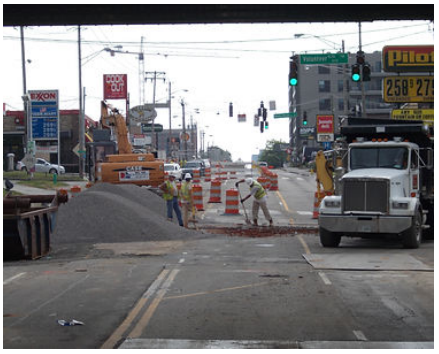

FEWER ONE-WAY STREETS IN CUMBERLAND AVENUE CORRIDOR SOON WILL GIVE MOTORISTS MORE OPTIONS

June 12, 2015

Starting Monday, motorists will be seeing more orange barrels around the Cumberland Avenue Corridor. But for those eager for a quicker commute through the City's reconstruction zone, these barrels signal an improvement that's coming soon.

Crews with the City's contractor, Southern Constructors, will be reworking the traffic flow on streets feeding into the eastern end of Cumberland Avenue. Four streets will be converted from one-way to two-way traffic – 18th, 19th, Mountcastle and 21st Street – between Lake and White avenues. (There is already two-way traffic on 20th Street.)

Orange barrels will go up over the next two weeks as a safety measure to allow drivers to become accustomed to the new traffic patterns while lanes are restriped and other steps are taken to assure a safe change-over from one-way to two-way traffic. **MORE >>>**

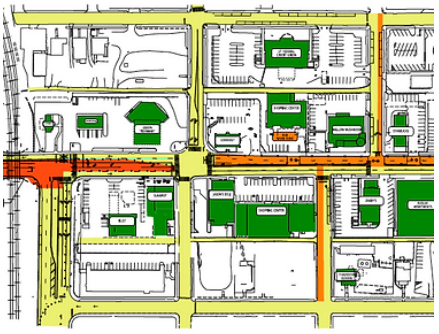

CUMBERLAND AVENUE LANES TO CLOSE AS NEXT STEP IN RECONSTRUCTION STARTS JUNE 9

June 4, 2015

For six weeks beginning Tuesday, June 9, all eastbound lanes of Cumberland Avenue between University Commons and West Volunteer Boulevard will be closed – the next step in a $17 million reconstruction.

During this period, one westbound lane of traffic will remain open (except for one complete weekend closure to rebuild the railroad crossing). There will be no westbound left turns onto Cumberland from West Volunteer Boulevard.

Crews will be installing a new 42-inch storm sewer pipe approximately 12 feet below the roadway, which will trigger the lane closures.

TRAFFIC UPDATE

June 1, 10:12 a.m.

LANE TO CLOSE ON SECTION OF 22ND STREET

Beginning at 7 a.m. Tuesday, June 2, workers will be installing a water valve at the intersection of 22nd Street and White Avenue.

The work will necessitate the closure of a section of the northbound lane of 22nd Street until 6 p.m. Wednesday, June 3.

Traffic will be open in both directions of 22nd, with flaggers

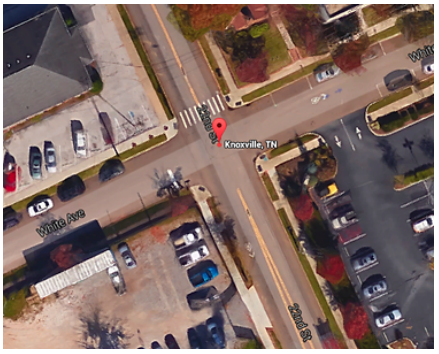

directing motorists around the work area. Traffic on White Avenue will be affected at the intersection, but it should be minimized by the flaggers.

The utility work is part of ongoing construction on the City's Cumberland Avenue Corridor Project. The intersection of 22nd and Cumberland remains closed, so Tuesday's closure of a lane on northbound 22nd only affects local traffic accessing businesses in that block of Cumberland Avenue.

Businesses up and down Cumberland Avenue remain accessible either from Cumberland or from side streets. Remember, there is free public parking on weekends and after 6 p.m. weekdays in the Fort Sanders Regional Medical Center lot at 19th Street and White Avenue and in the UT Federal Credit Union lot at 22nd Street and White Avenue.

Two Week Look Ahead

Update on May 28, 2015 10:50 a.m.

The following is a two week look ahead:

- Installation of Inserta Valves at 22nd Street and White
- Final testing of water lines Week of June 1
- Water services and fire line connections in 22nd Street
- **Completion of Phase I of the KUB utilities relocation from Volunteer to 22nd is on schedule**
- **Phase I of the Streetscapes begins June 8.**

New traffic patterns changes will begin June 9. More information will be posted Week on June 1.

Cumberland Avenue Has Been Reopened

May 24, 2015 8:22 a.m.

Cumberland Ave. is now open for through traffic. The water line crossing went well and ahead of anticipated schedule.

Have a safe holiday weekend and remember to honor the memory of those who gave their life for the freedom we now enjoy.

Two Week Look Ahead

Updated May 21, 2015 10:45 a.m.

The following is a two week look ahead:

- The completion of water, sewer and gas connections within 22nd Street intersection
- Completion of water line installation on 22nd Street North
- Installation of water valves at 22nd Street and White Avenue

The Phase I Streetscapes begins June 8, 2015. We will post information on the new traffic pattern that will be implemented for Phase I of the Streetscapes construction. Installation of traffic control devices to begin on or about June 8, 2015.

CUMBERLAND AVENUE CLOSED THIS WEEKEND AT 22ND STREET

Updated May 20, 2015 745 a.m.

As part of ongoing construction on the City's Cumberland Avenue Corridor Project, all lanes of Cumberland Avenue will be closed to traffic this weekend at its intersection with 22nd Street.

>>>>In order to allow the installation of a water line from north to south across Cumberland, the 22nd Street intersection will be closed from 10 p.m. Friday, May 22, until 6 a.m. Monday, May 25.

>>>>Both eastbound and westbound traffic should detour along West Volunteer Boulevard and Lake Avenue (see attached detour map). The detour will be clearly marked with road signs.

>>>>Businesses along Cumberland Avenue will remain accessible either from Cumberland or from side streets. Remember, there is free public parking on weekends and after 6 p.m. weekdays in the Fort Sanders Regional Medical Center lot at 19th Street and White

Avenue, and in the UT Federal Credit Union lot at 22nd Street and White Avenue.

DOWNLOAD DETOUR MAP FOR WEEKEND CLOSURE HERE.

TRAFFIC ALERT UPDATE! Extended Lane Closure on 17th Street

Updated May 20, 2015, 7:43 a.m.

Due to the rainy weather the work on 17th Street at Dale Avenue has been delayed.

There will be an outside, northbound lane closure on 17th Avenue at the north end of the bridge between Grand Avenue and Dale Avenue until Friday, May 22 at 6pm. The closure is for the contractor to remove and replace curb and gutter at the end of the bridge.

A section of 22nd Street will be closed at its intersection with Cumberland Avenue starting Monday, May 11.

May 11, 2015

To make water and sewer connections at 22nd Street north and south of Cumberland, the contractor will need to close 22nd Street between Cumberland and White Avenue. There will be limited access to the 22nd Street entrances to the Cook Out and Exxon properties. The closure is expected to last approximately four weeks.

22nd Street north of White Avenue will remain open.

During the same period, the work will require lane closures on 22nd Street south of Cumberland, but traffic will be maintained.
